

SKANSKA



STRABAG

Working on
behalf of

HS2

SCSJV works update

Community representatives meeting - 25 January 2021

Current works – Crossover Box and Flat Iron sites


Crossover Box site

- Construction of site on-site roads, working platforms and drainage
- Ongoing works to set up site welfare and office facilities
- Excavation of ventilation shaft

Flat Iron site

- Works to upgrade vehicle holding area including:
 - Removal of concrete slab
 - Drainage surveys
 - Road resurfacing and line markings
 - Installation of new barriers and gates


The approximate location of these works is shown on the map to the right

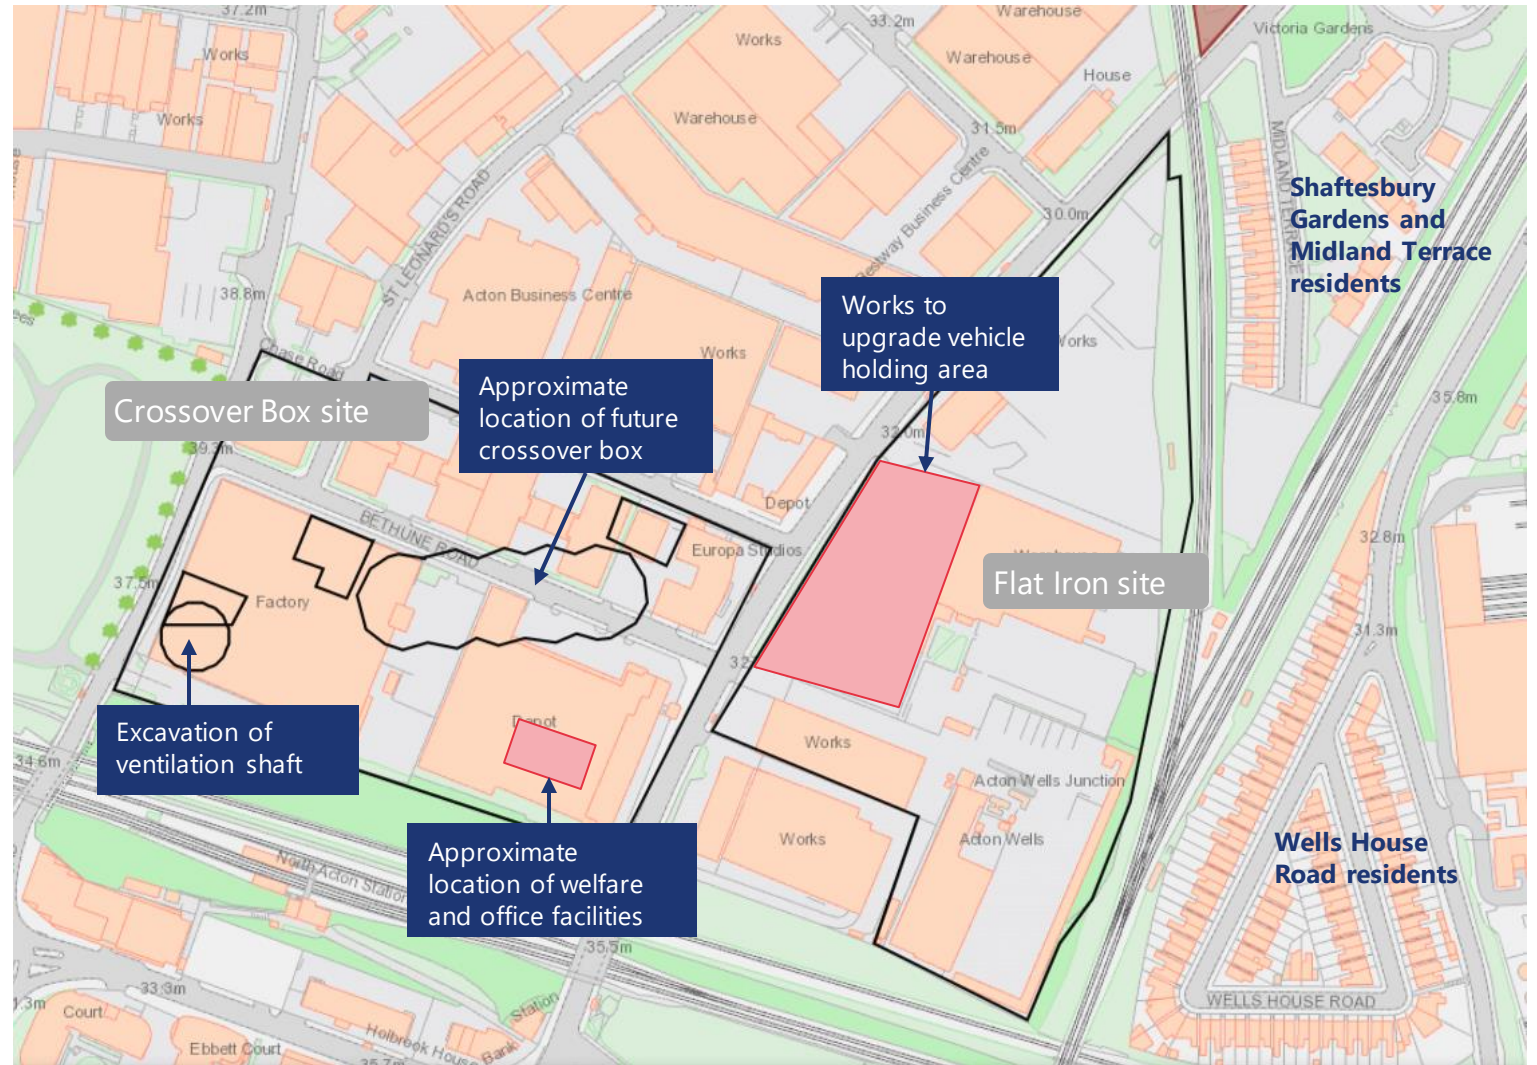

Current works - Atlas Road site

- Construction of on-site roads and drainage
- Changes to the site entrance and road layout on Atlas Road (near bus depot)
- Building abutments / foundations in Grand Union Canal embankment for temporary bridge
- Ground investigations and works to install foundations for future welfare facilities
- Preparations for future piling works
- Preparations to build storage areas for future tunnel segments


The approximate location of these works is shown on the map to the right

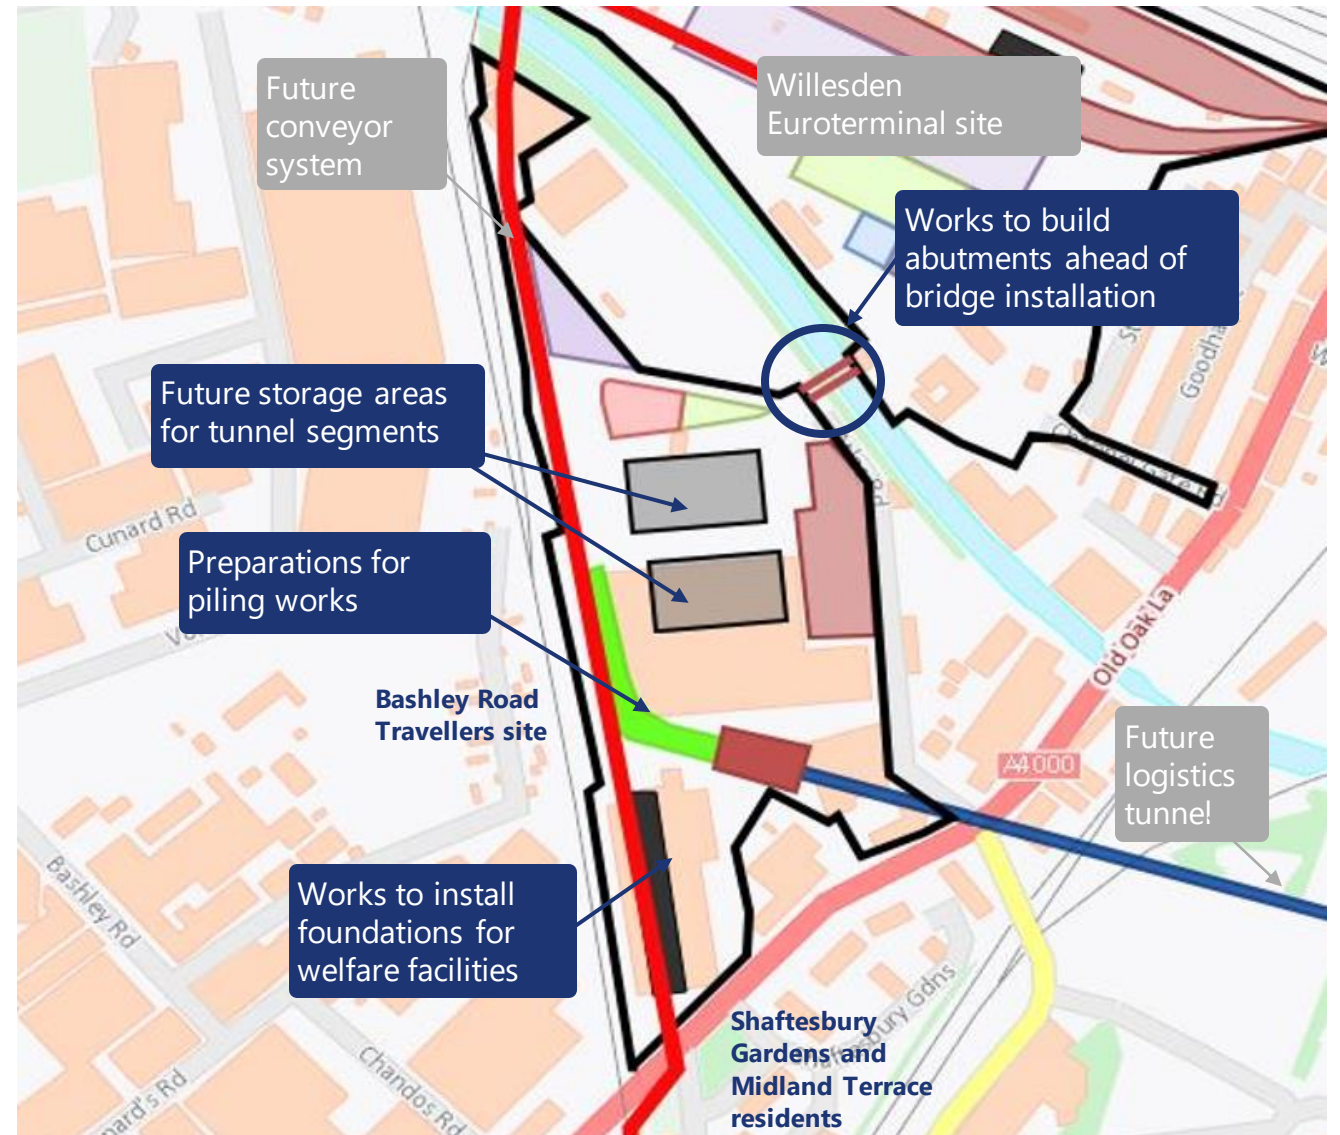

Current works – Willesden Euroterminal site

- Construction of on-site roads and drainage
- Ground investigations
- Works to upgrade to rail infrastructure
- Works to build material storage areas
- Refurbishing the existing building ('Bread bin') to set up our logistics hub
- Build foundations / abutments for temporary Grand Union Canal bridge
- Installation of fencing along Channel Gate Road
- Preparing to install pedestrian footbridge within site

The approximate location of these works is shown on the map to the right

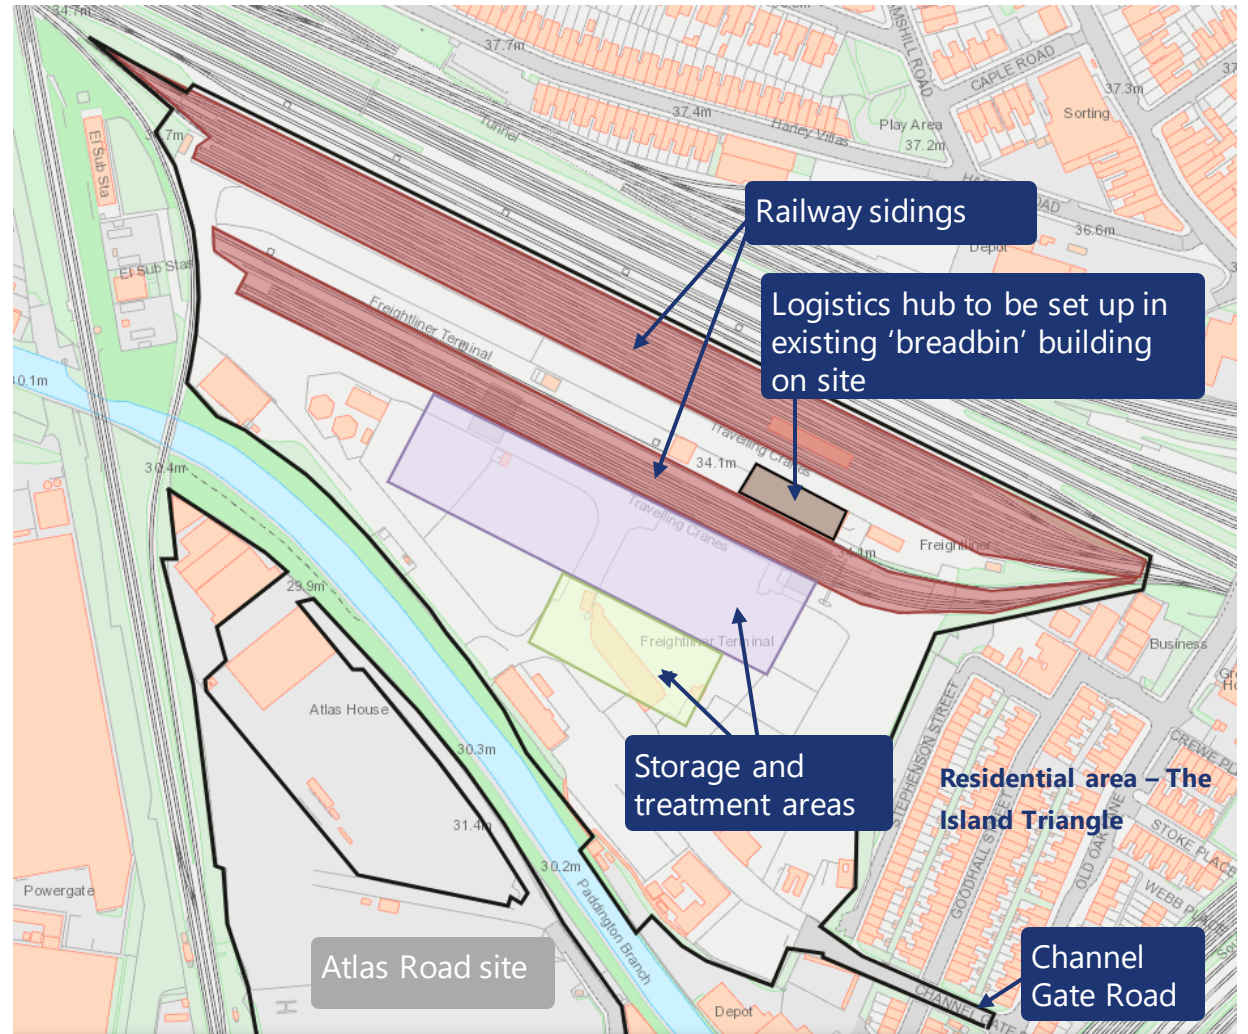


Installation of temporary bridge – 18 to 21 February

To safely lift the temporary Grand Union Canal bridge into place, we will need to temporarily close a small section of the canal towpath for four days from 18 to 21 February*.


A signed diversion route will be in place for pedestrians and cyclists on the above dates.

We have written to local residents about these works - the notification is available at [HS2inOldOak.co.uk](https://www.hs2inoldoak.co.uk)

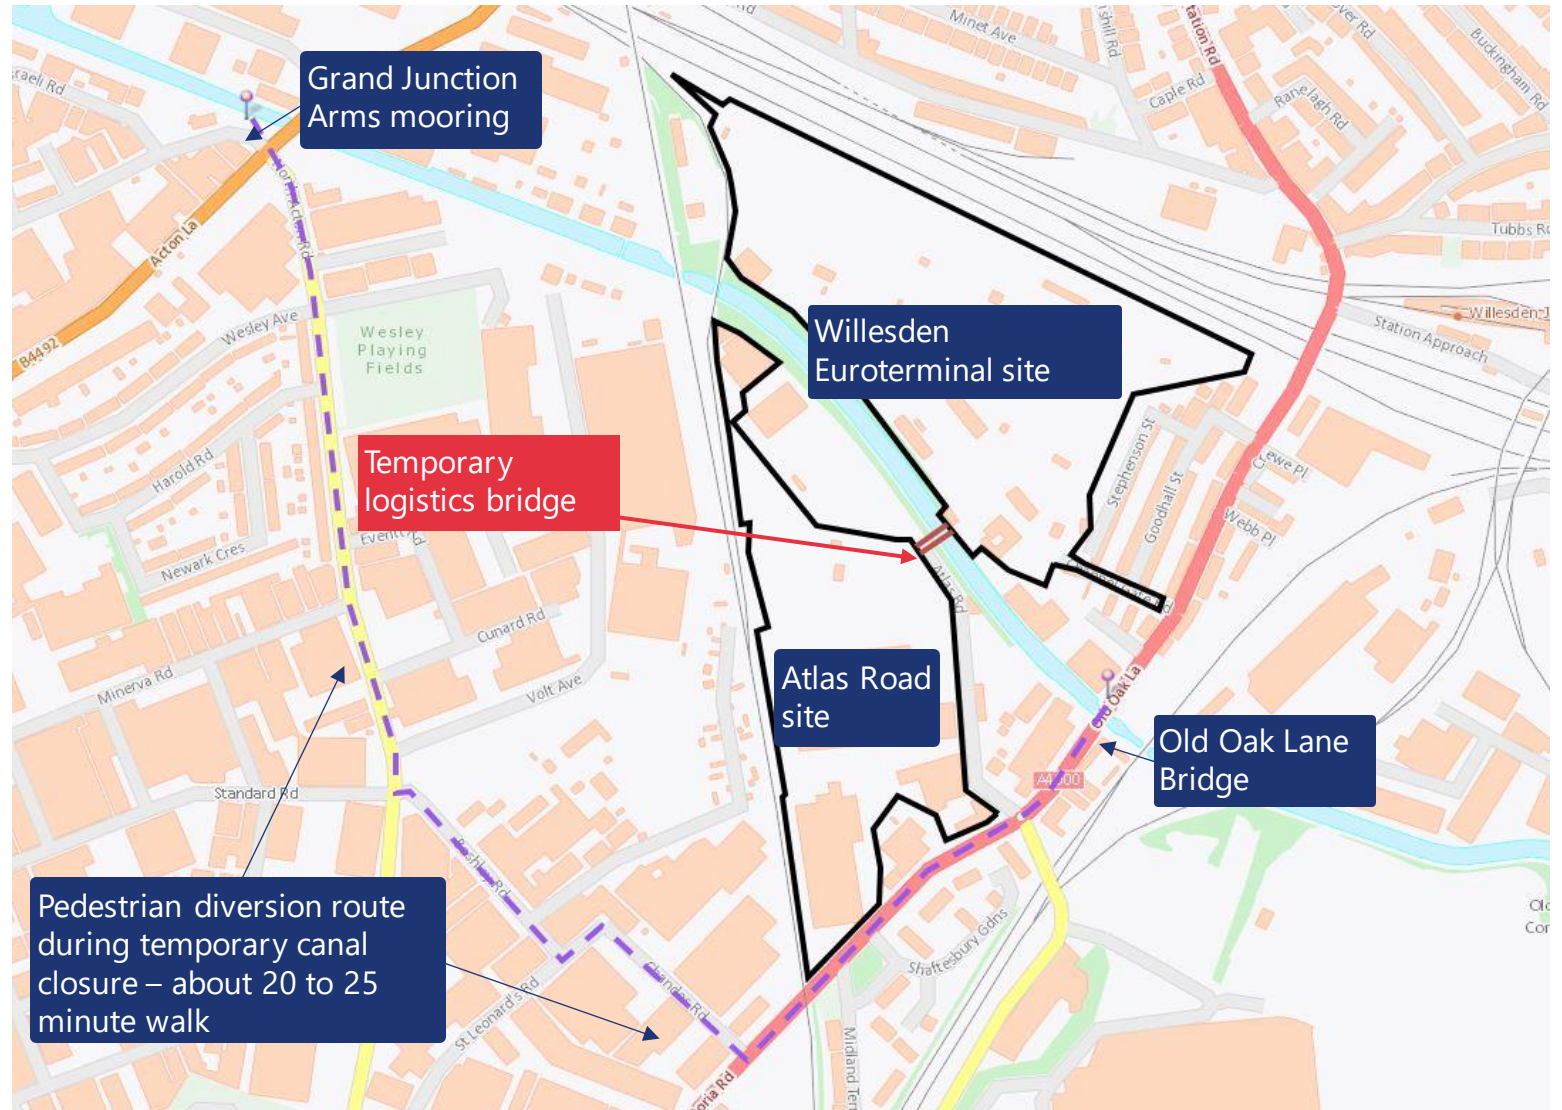

*Our construction programme remains subject to change


Visualisation of temporary bridge

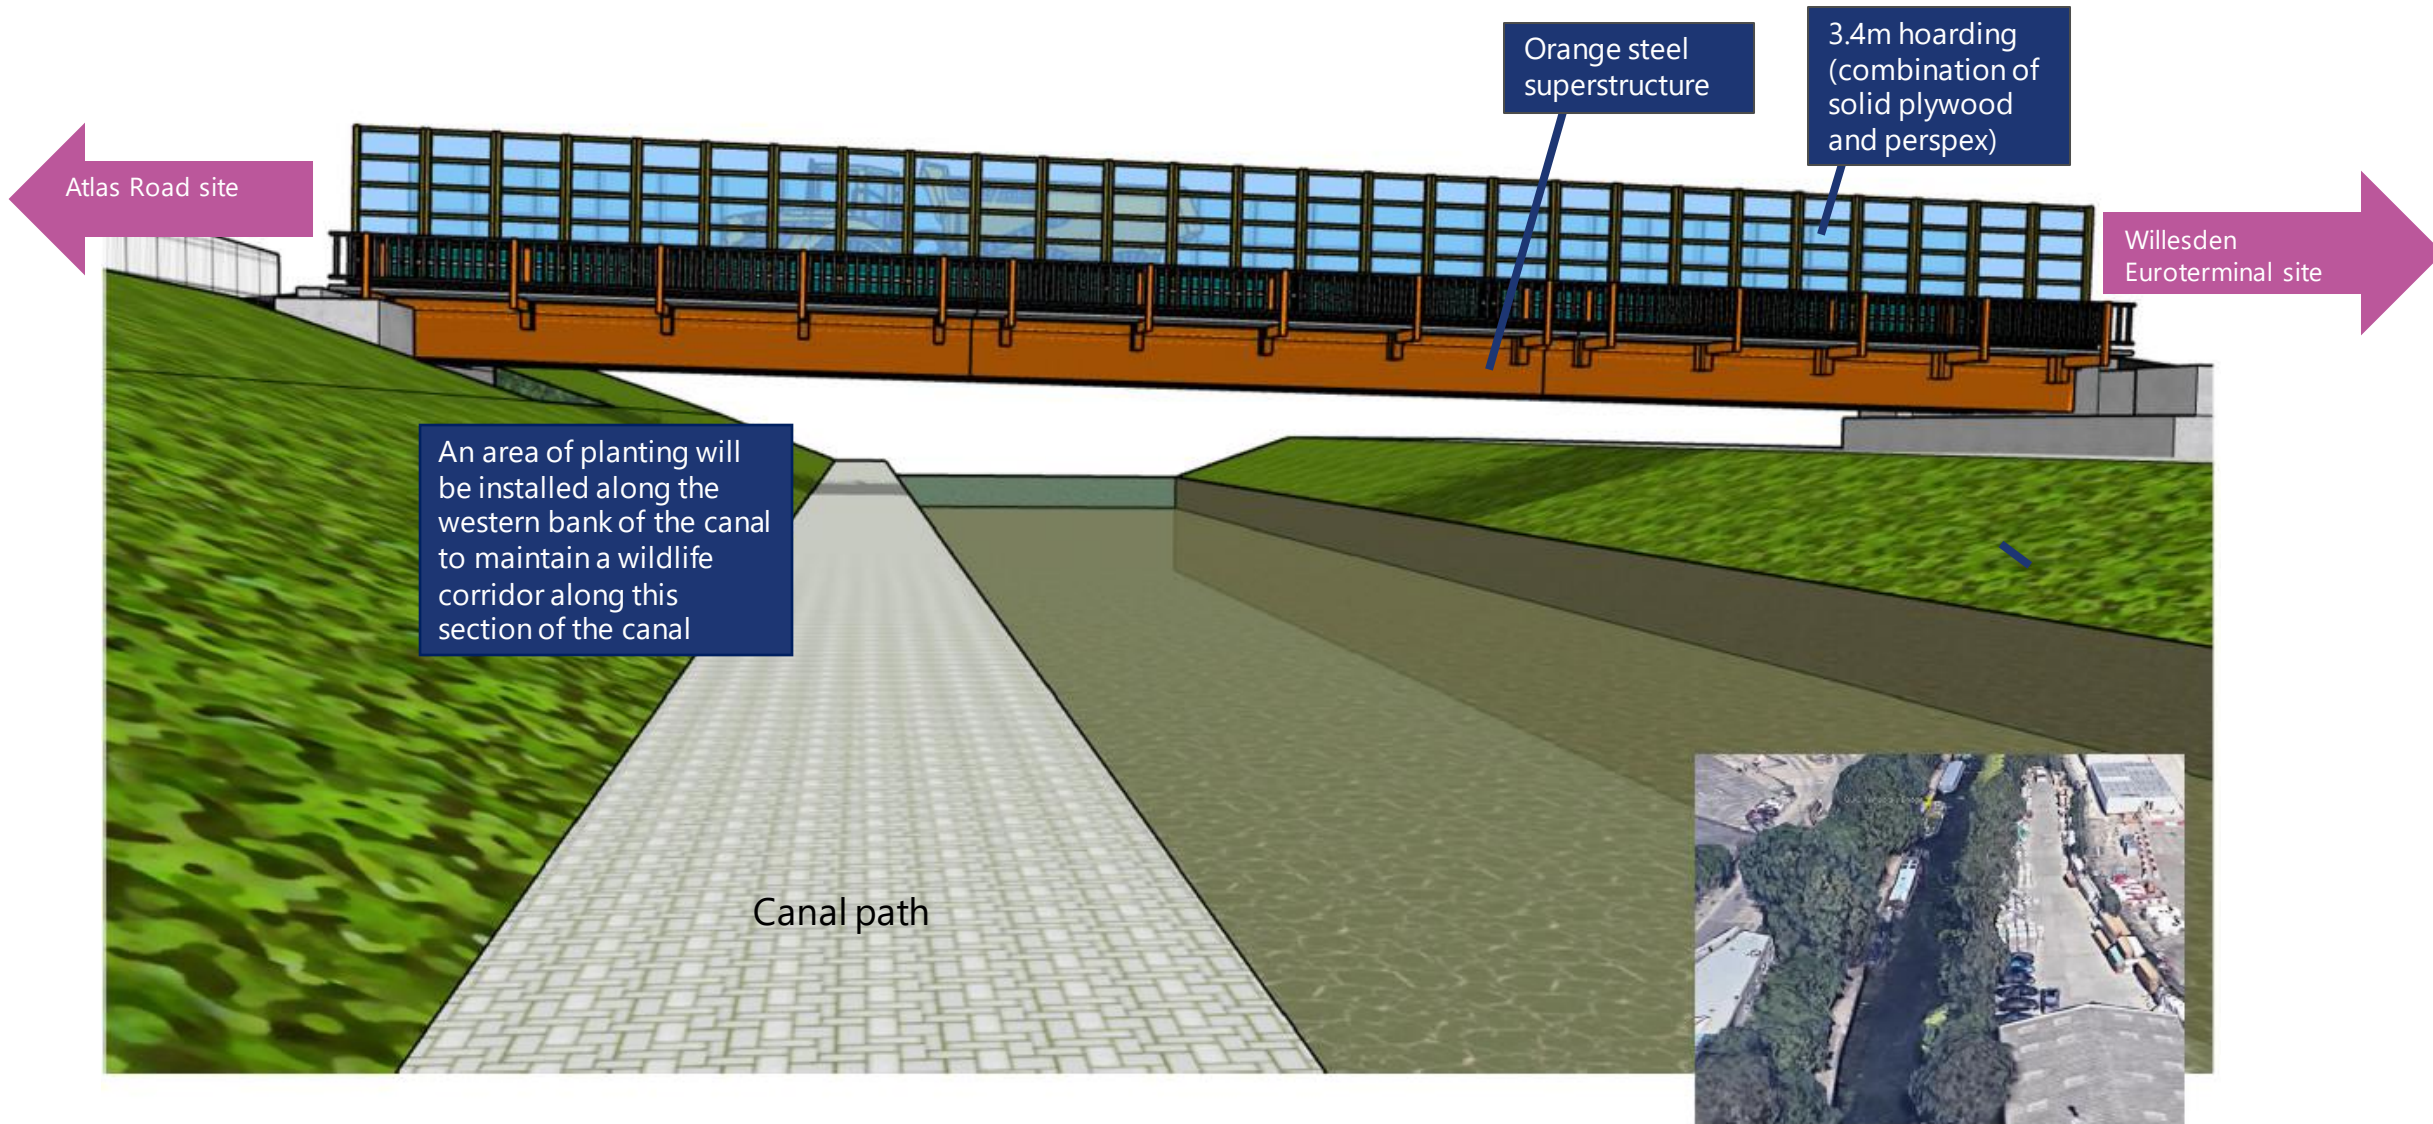

Visualisation of temporary bridge

3.4m hoarding
(combination of
solid plywood and
perspex)

Willesden Euroterminal site

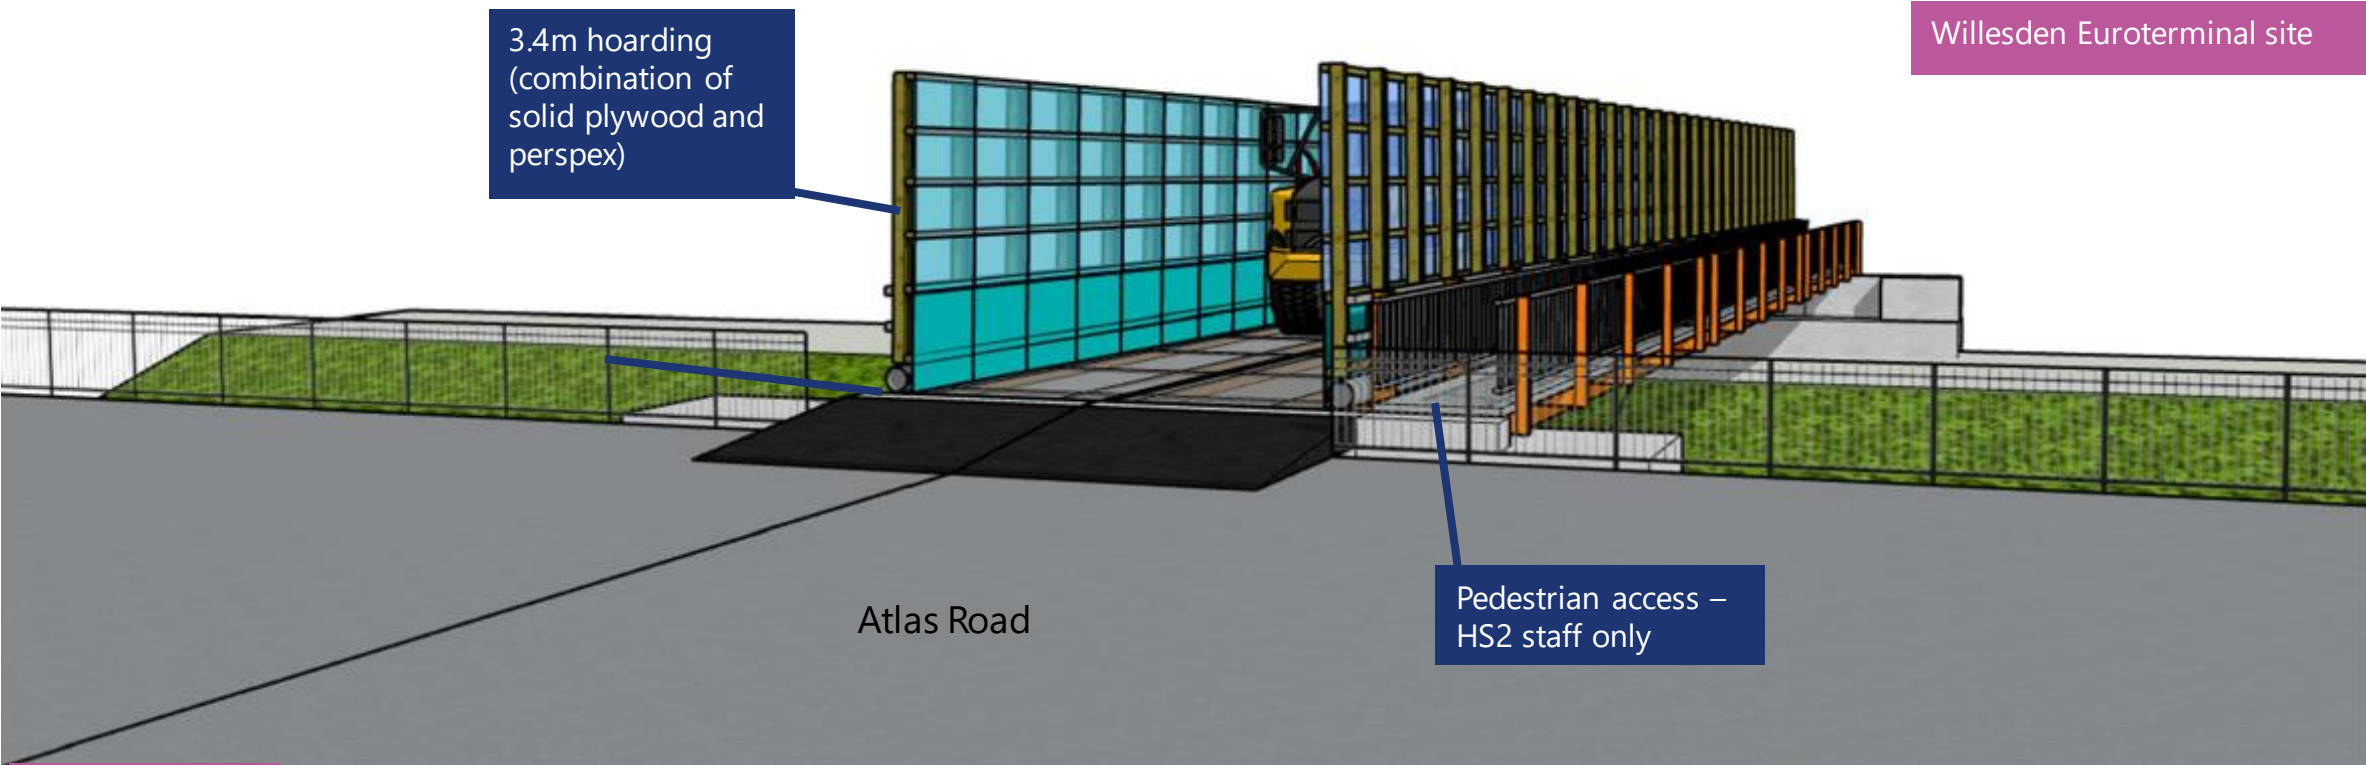

Atlas Road

Pedestrian access –
HS2 staff only

Atlas Road site



Works planned from February to April 2021*

Site	February 2021	March 2021	April 2021
Victoria Road Crossover Box site	<p>Construction of ventilation shaft</p> <p>Ongoing construction of on-site roads, drainage systems and backfilling of excavations</p> <p>Construction of permanent platform for welfare</p> <p>Completion of vehicle holding area upgrades</p> <p>Installation of temporary site services</p>	<p>Construction of ventilation shaft</p> <p>Ongoing construction of on-site roads, drainage systems and backfilling of excavations</p> <p>Installation of permanent welfare units</p> <p>Installation of temporary site services</p> <p>Construction of concrete slab for bentonite plant and bending yard</p> <p>Preparation for piling works including set up of piling rig</p>	<p>Construction of ventilation shaft (possible extension of working hours, to be confirmed)</p> <p>Ongoing construction of on-site roads, drainage systems and backfilling of excavations</p> <p>Installation of conveyor bases</p> <p>Start piling works for crossover box</p> <p>Installation of muck bin</p> <p>Set up bentonite plant and bending yard</p>
Flat Iron site	<p>Ongoing works to upgrade vehicle holding area (Flat Iron site)</p>	<p>Installation of new security gates and vehicle route (Flat Iron site)</p>	<p>Installation of conveyor bases</p>

*these dates may change. We'll keep residents updated about our works and provide updates at [HS2inOldOak.co.uk](https://www.hs2inoldoak.co.uk)

Works planned from February to April 2021*

Site	February 2021	March 2021	April 2021
Atlas Road site	<p>Ongoing construction of on-site roads and drainage and changes to site entrance / road layout on Atlas Road</p> <p>Completion of abutment works in canal embankment and installation of temporary Grand Union Canal bridge</p> <p>Works to install foundations and utility connections for future welfare facilities</p> <p>Install site offices and welfare facilities</p> <p>Preparation for piling works to build Atlas Road Logistics Tunnel launch box</p> <p>Construction of storage areas</p>	<p>Commence piling operations for logistic tunnel launch ramp and box</p> <p>Install site offices and welfare facilities</p> <p>Construction of storage areas</p> <p>Preparation for piling works to build Atlas Road Logistics Tunnel launch box</p>	<p>Piling operations for logistic tunnel launch ramp and box</p> <p>Installation of conveyor bases</p> <p>Construction of storage areas</p> <p>Installation of gantry crane foundations</p> <p>Starting of piling works to build Atlas Road Logistics Tunnel launch box</p>
Willesden Euroterminal site	<p>Completion of abutment works in canal embankment and installation of temporary Grand Union Canal bridge</p> <p>Ongoing construction of on-site roads, drainage and storage areas</p> <p>Installation of pedestrian footbridge</p> <p>Refurbishing the existing building ('Bread bin') to set up our logistics hub</p> <p>Start receiving material from Old Oak Common Station site</p> <p>Ongoing works to upgrade rail infrastructure</p>	<p>Refurbishing the existing building ('Bread bin') to set up our logistics hub</p> <p>Ongoing construction of on-site roads and drainage</p> <p>Construction of gantry crane foundations and running beams / rails</p> <p>Ongoing works to upgrade rail infrastructure</p>	<p>Refurbishing the existing building ('Bread bin') to set up our logistics hub</p> <p>Ongoing construction of on-site roads and drainage</p> <p>Construction of gantry crane foundations and running beams / rails</p> <p>Installation of conveyor bases</p> <p>Completion of works to upgrade rail infrastructure</p>

*these dates may change. We'll keep residents updated about our works and provide updates at [HS2inOldOak.co.uk](https://www.hs2inoldoak.co.uk)

Any questions?

