SKANSKA COSTAIN STRABAG Working in partnership with HS2

Hampstead Road bridge construction

October 2026

Hampstead Road bridge construction

We need to extend Hampstead Road bridge to pass over the newly excavated and extended railway cutting. To keep traffic moving, we'll build a temporary road alongside Hampstead Road, over the area known as Zone 5 (see slide 6), to maintain an uninterrupted traffic flow on Hampstead Road while we extend the bridge. We will carry out these works in phases until 2031.

The first phase will run from **October 2026** to **spring 2027** . During this phase we will build the temporary road in Zone 5 and then connect it to Hampstead Road. After finishing preparatory works, we'll **close off northbound traffic** on Hampstead Road on the nights of **21 and 22 November** to paint the road lines and install cycle bollards . After we build the temporary road in Zone 5, we will need to fully close Hampstead Road to connect the temporary road. We expect this to happen in spring 2027.

We previously told you that we would need to fully close Hampstead Road for four weeks. We have worked hard to **reduce the closure to one week** and can confirm:

- We'll close Hampstead Road overnight only for the first four nights, from Monday to Thursday
- We'll then fully close Hampstead Road from Friday evening until Monday morning
- The closure will extend from Harrington Square in the north to Robert Street in the south

Hampstead Road bridge construction

We'll aim to complete most noisy activities during the day. However, some noisy work can only be done once we close the road. Note that the dates may change, and we will confirm closure dates and details of traffic and bus diversions nearer the time.

After the first full closure, we'll need to close Hampstead Road on two more occasions, for about four weeks each in 2028 and 2030. The table on the next slide shows the work phases. Please note that dates may change, and we will keep you updated.

We understand these closures will impact the local community and we are looking at ways we can reduce the impacts, including durations of the road closures. We will confirm dates of the closures closer to the time.

Programme

Phase	Activity	Date
0	Preparatory works in Zone 5	June to October 2026
1	Temporary road construction, traffic switched to northbound lane	October 2026 to Spring 2027
2	**Full closure** of Hampstead Road (now reduced to one week)	Spring 2027
3	Temporary road in use while constructing the northbound bridge deck	Spring 2027 to November 2028
4	**Full closure** of Hampstead Road to tie-in northbound carriageway to existing road	December 2028 to January 2029
5	Removal of temporary road with traffic on northbound bridge deck	January to April 2029
6	Southbound bridge deck construction (traffic on northbound bridge deck)	April 2029 to May 2030
7	**Full closure** of Hampstead Road to connect northbound and southbound bridge decks	June to July 2030
8a	Base slab construction under the bridge	July 2030 to December 2031
8b	Finishing works	June 2030 to December 2031

Keeping you informed

Regular engagement events

- Construction Update events – March and September
- Rooftop guided tour – March and September

Hampstead Road bridge focused engagement


- Drop-in events at the Euston Community Hub
- Regular notifications sent to local community

Text messaging service


- Should you wish to receive our SMS updates please complete a short online form by scanning the QR code above and providing your name, contact number and street name.

You can sign up to receive updates about HS2 works in your local area at www.hs2inyourarea.co.uk


Hampstead Road bridge – Phase 0 – Works inside Zone 5

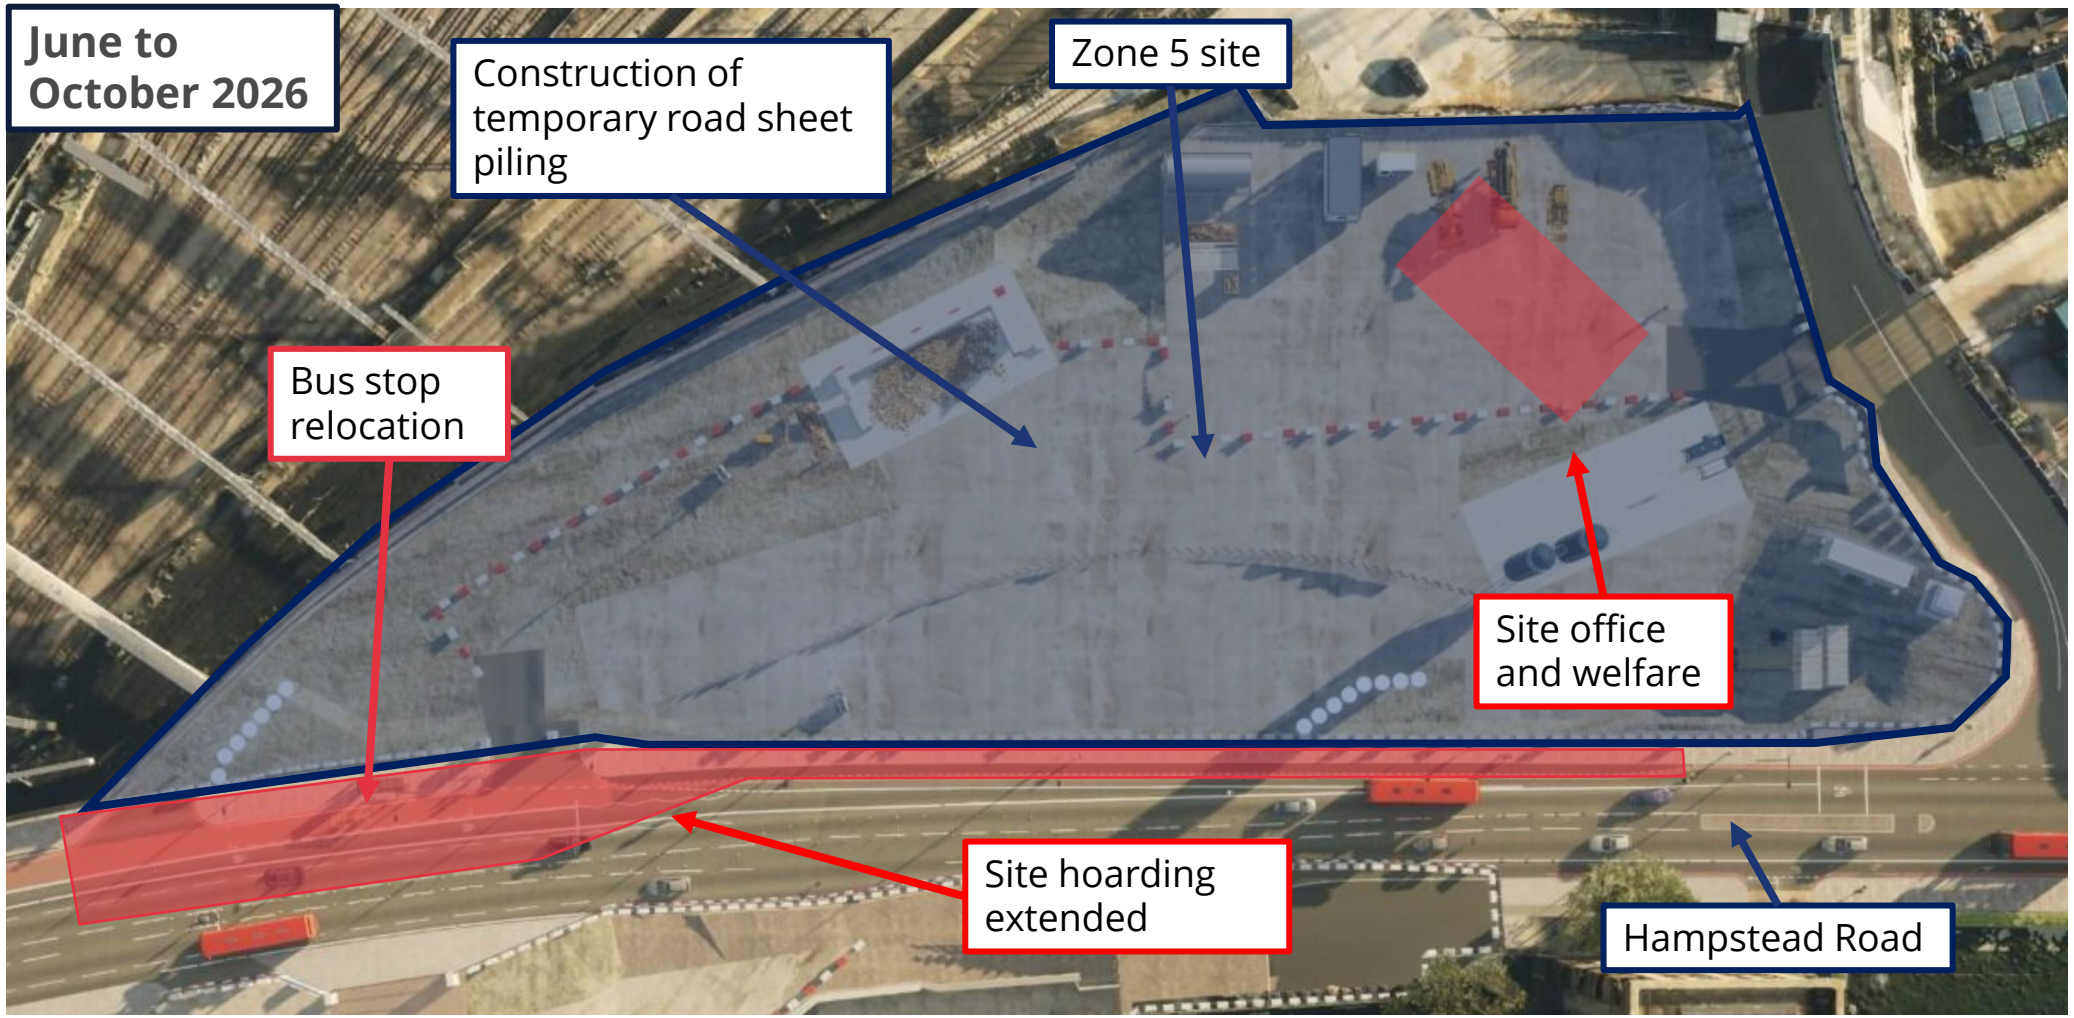

Hampstead Road bridge – Phase 1 road layout

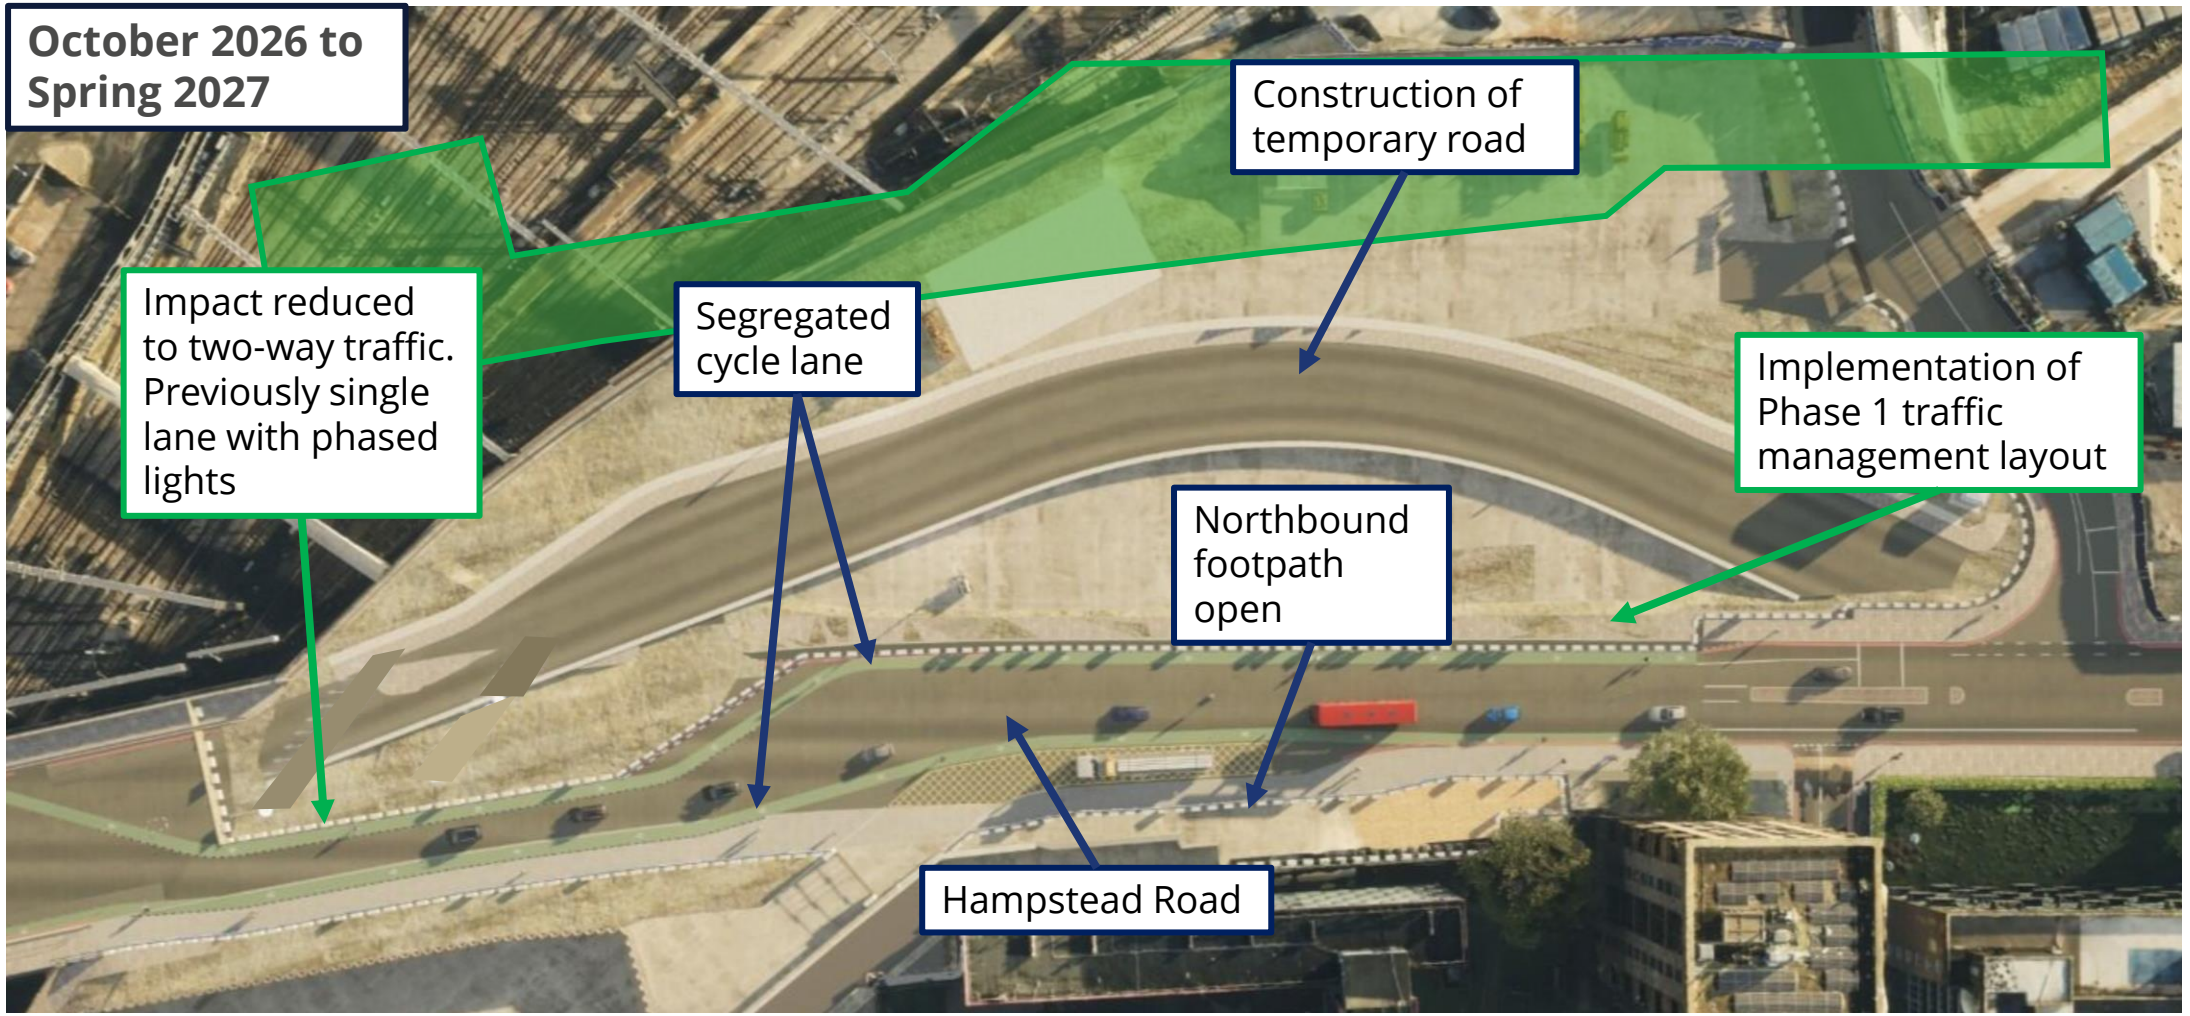


Hampstead Road bridge – Phase 1 traffic management - Northbound

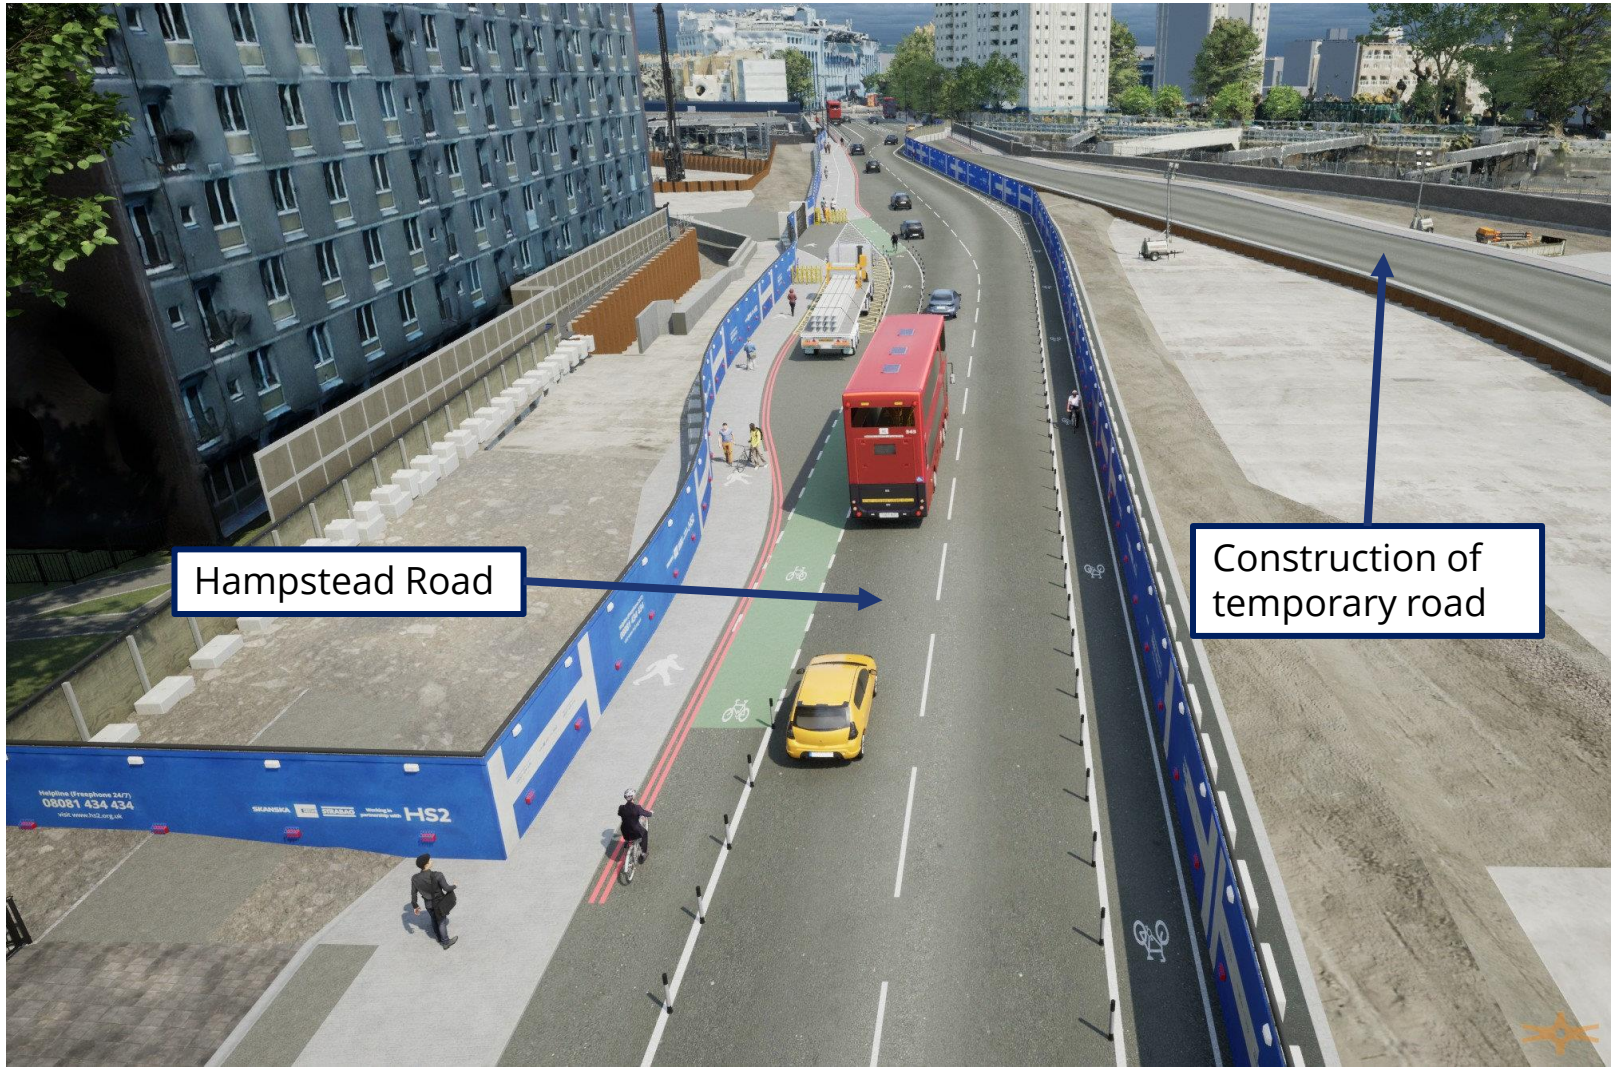


- Traffic maintained in both directions
- Pedestrians to use northbound footpath
- Segregated cycle lane in both directions

Hampstead Road bridge – Phase 1 traffic management - Southbound

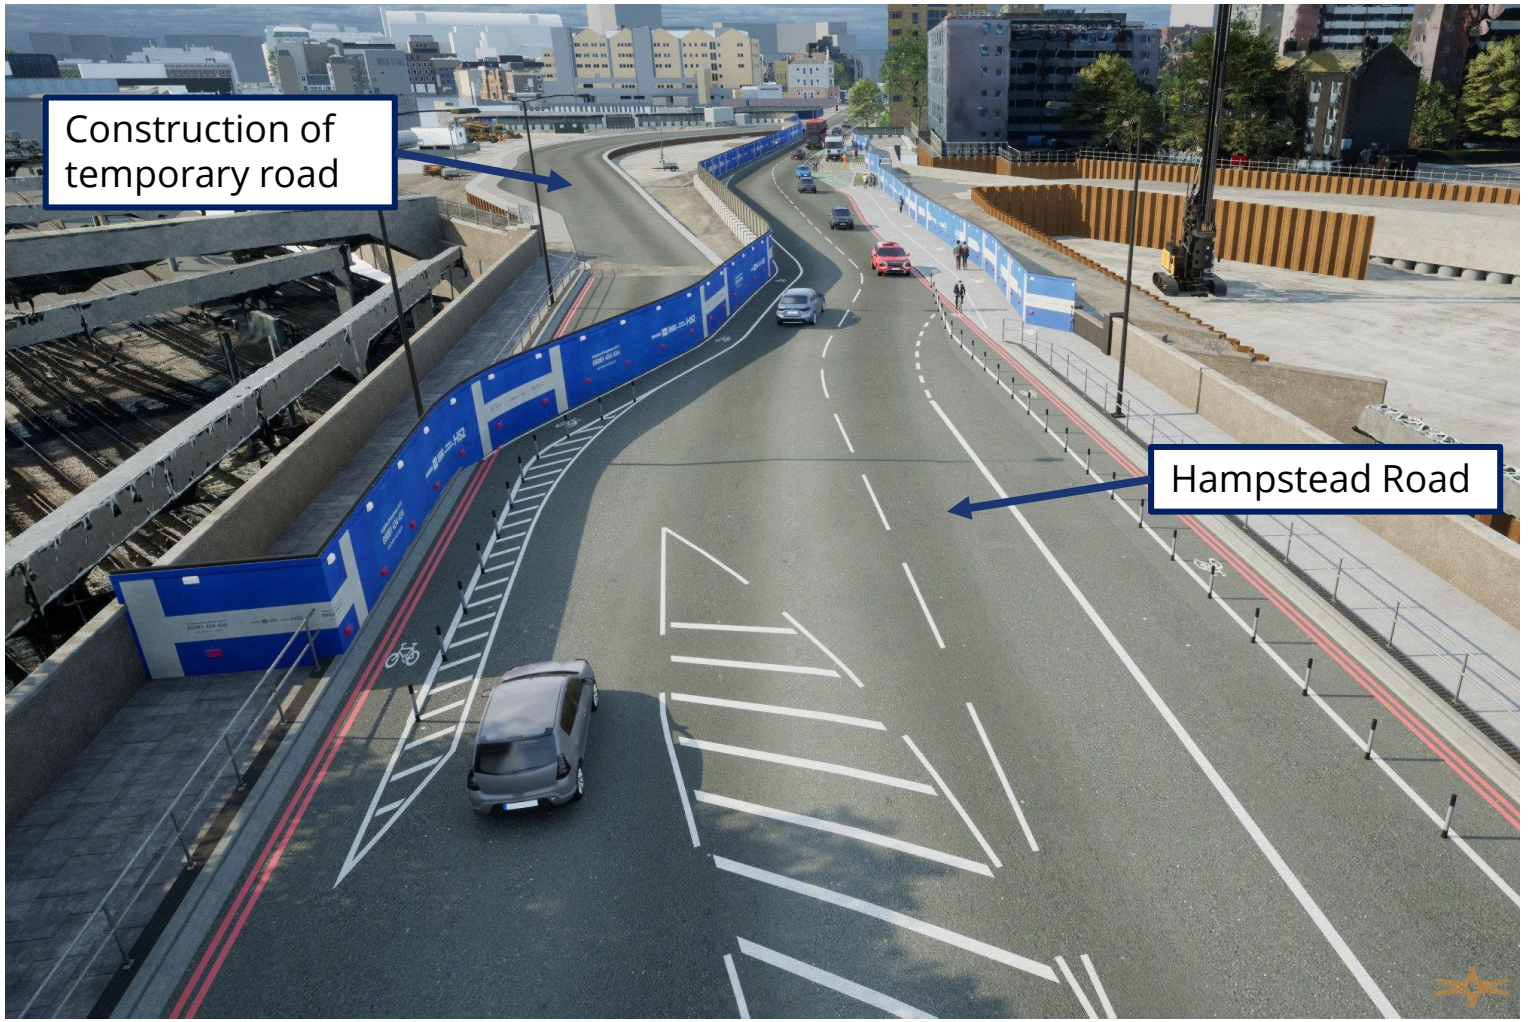


- Traffic maintained in both directions
- Pedestrians to use northbound footpath
- Segregated cycle lane in both directions
- Bus stop W relocated 80m north, closer to Ampthill Estate

Hampstead Road bridge – Phase 2 – Road closure for temporary road connection works

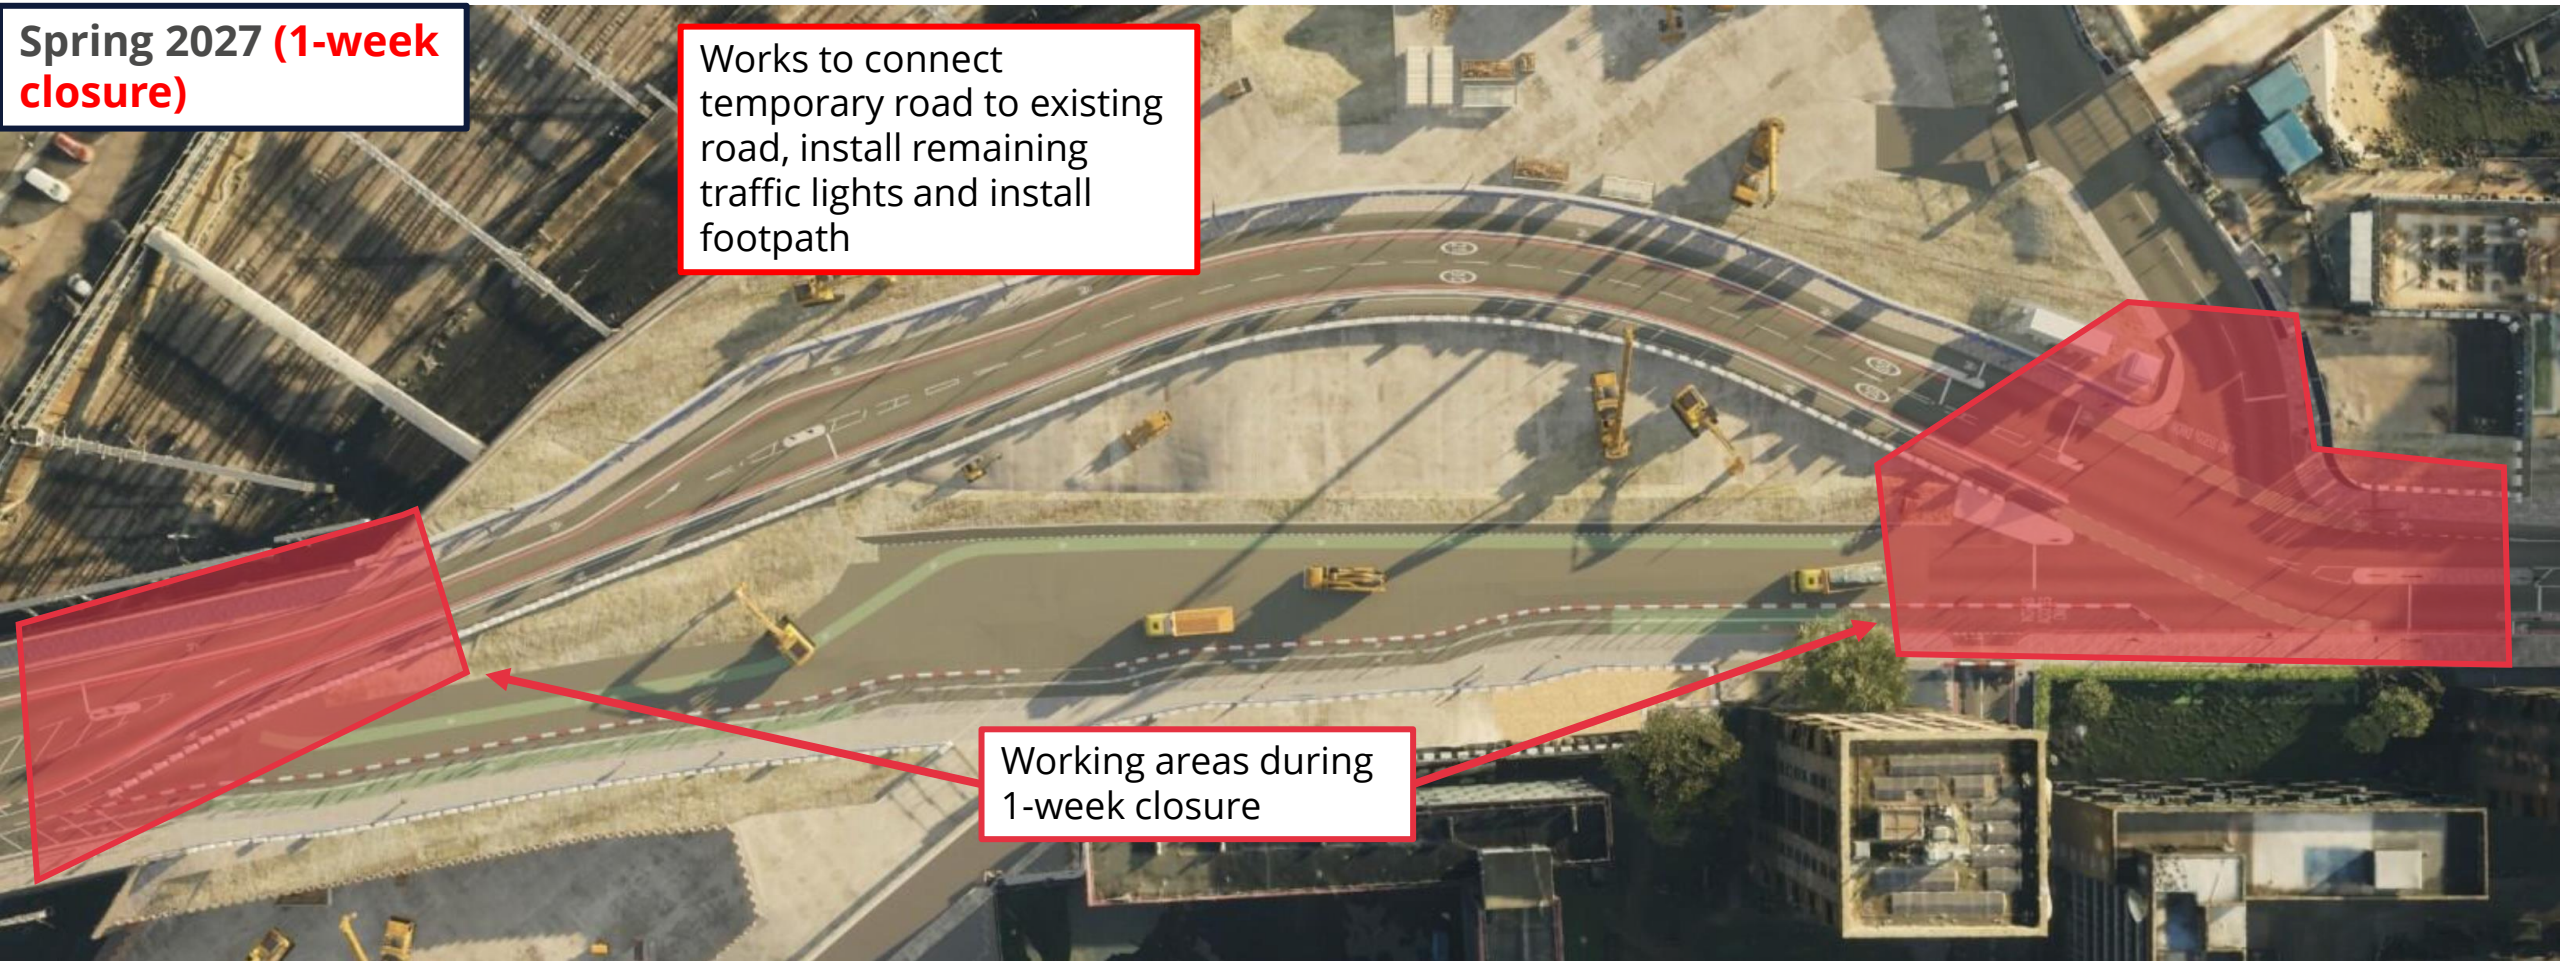


Hampstead Road bridge – Phase 3 – Temporary road in use

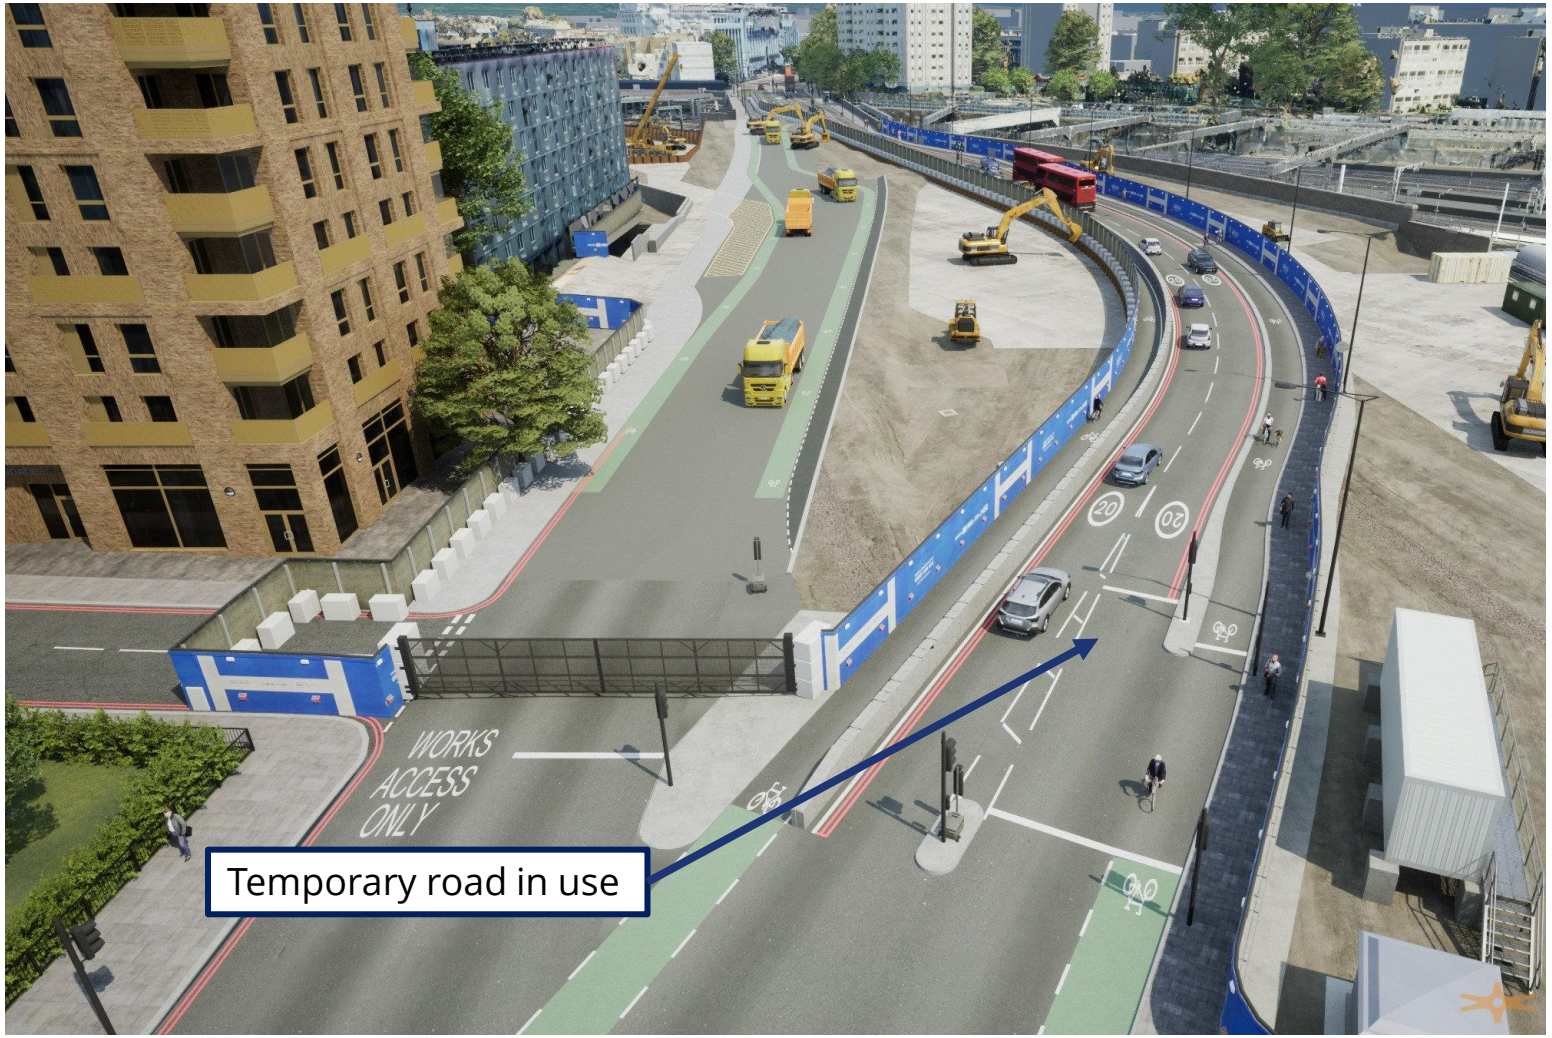


- Traffic maintained in both directions
- Pedestrians to use southbound footpath
- Segregated cycle lane in both directions

Hampstead Road bridge – Phase 3 – Temporary road in use

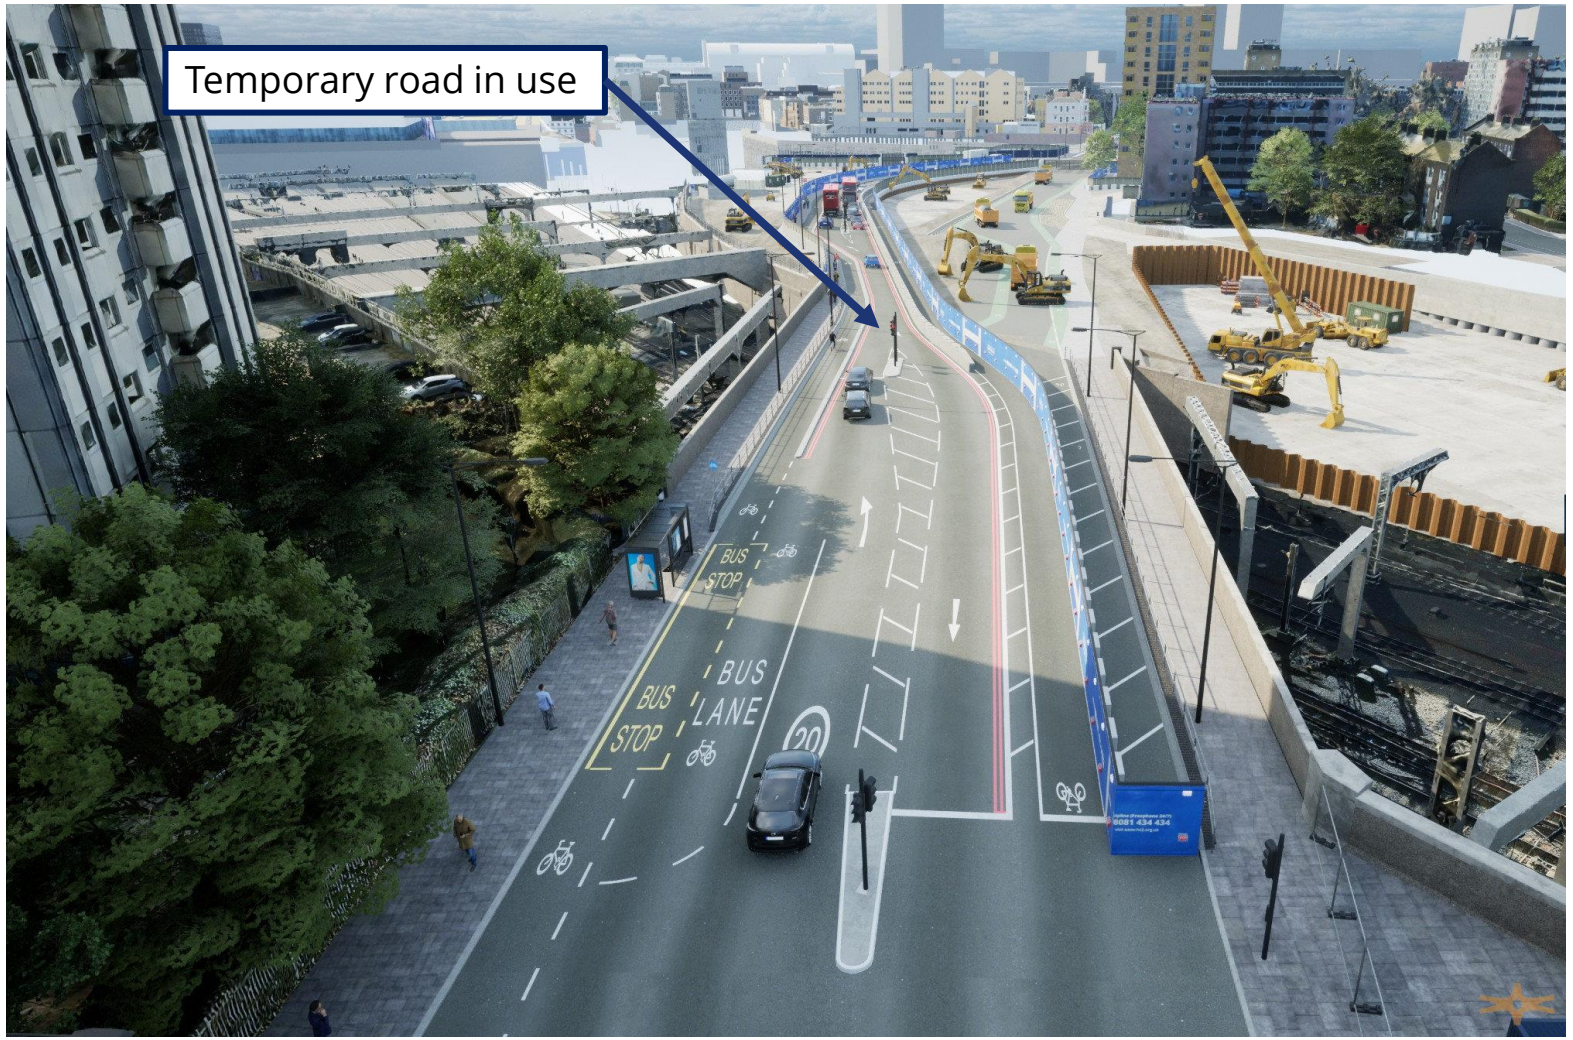

- Traffic maintained in both directions
- Pedestrians to use southbound footpath
- Segregated cycle lane in both directions


Hampstead Road bridge – Phase 3 – Construction of northbound bridge deck

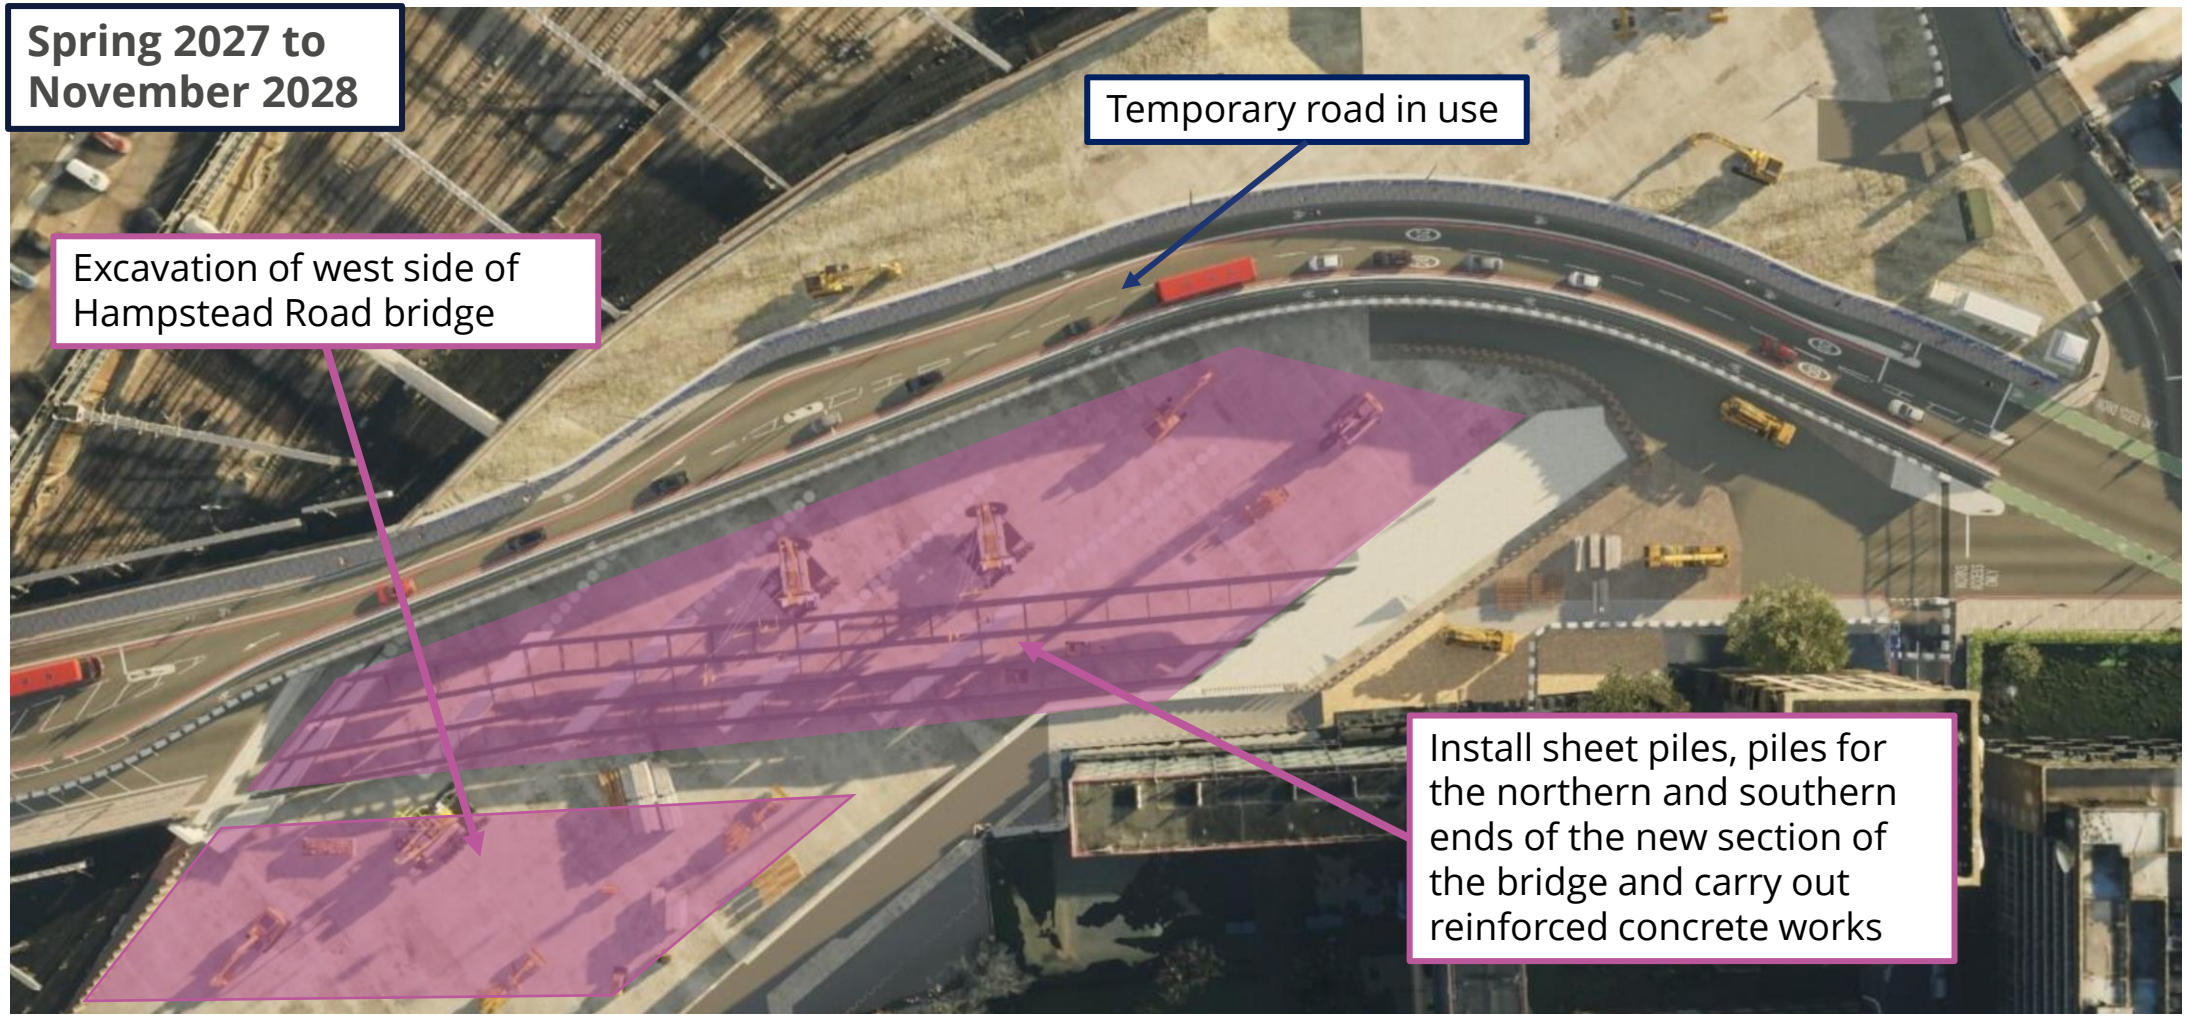


Phase 3 – Northbound deck construction




Hampstead Road bridge – Phase 3 – Construction of northbound bridge deck

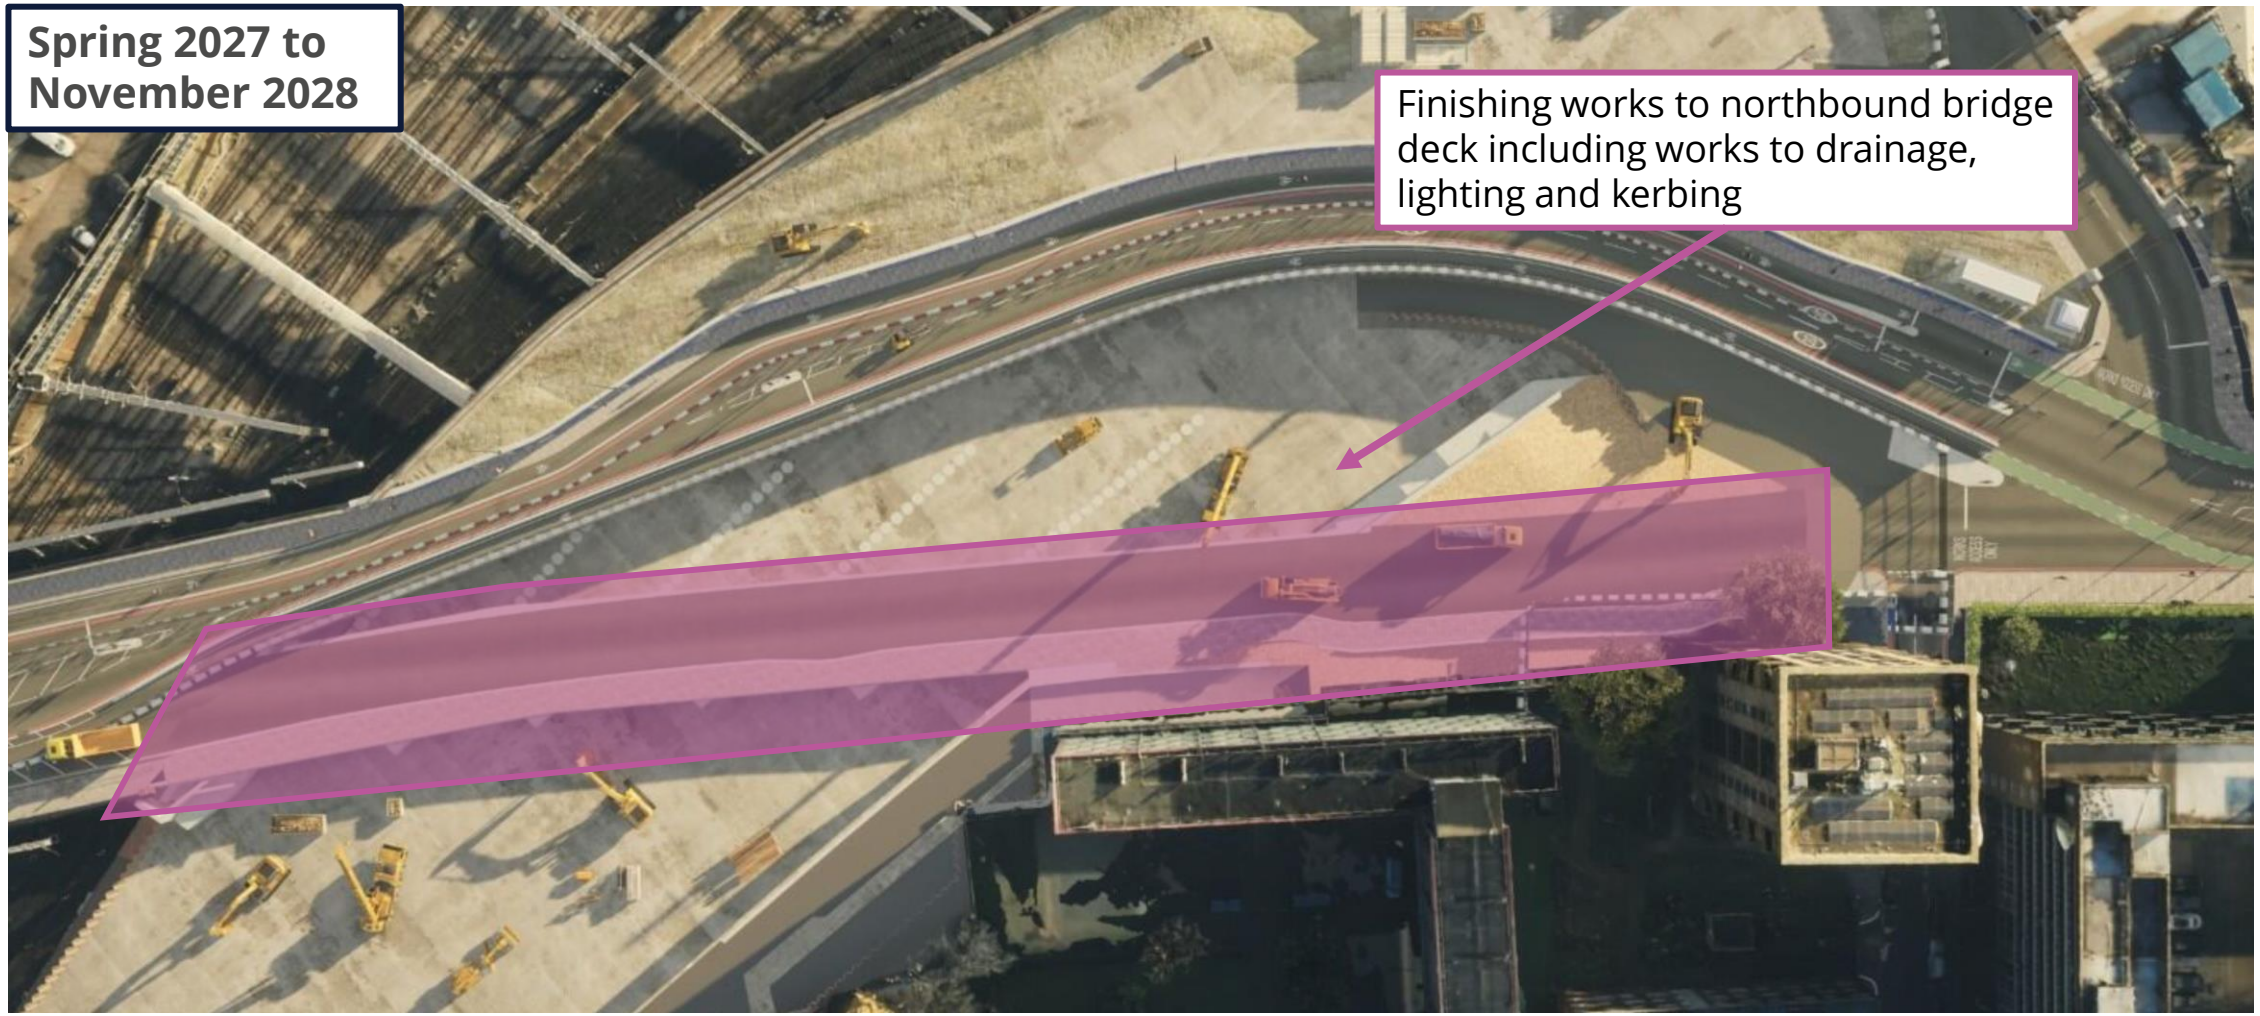


Hampstead Road bridge – Phase 4 – Northbound tie in. Traffic moves to northbound lane

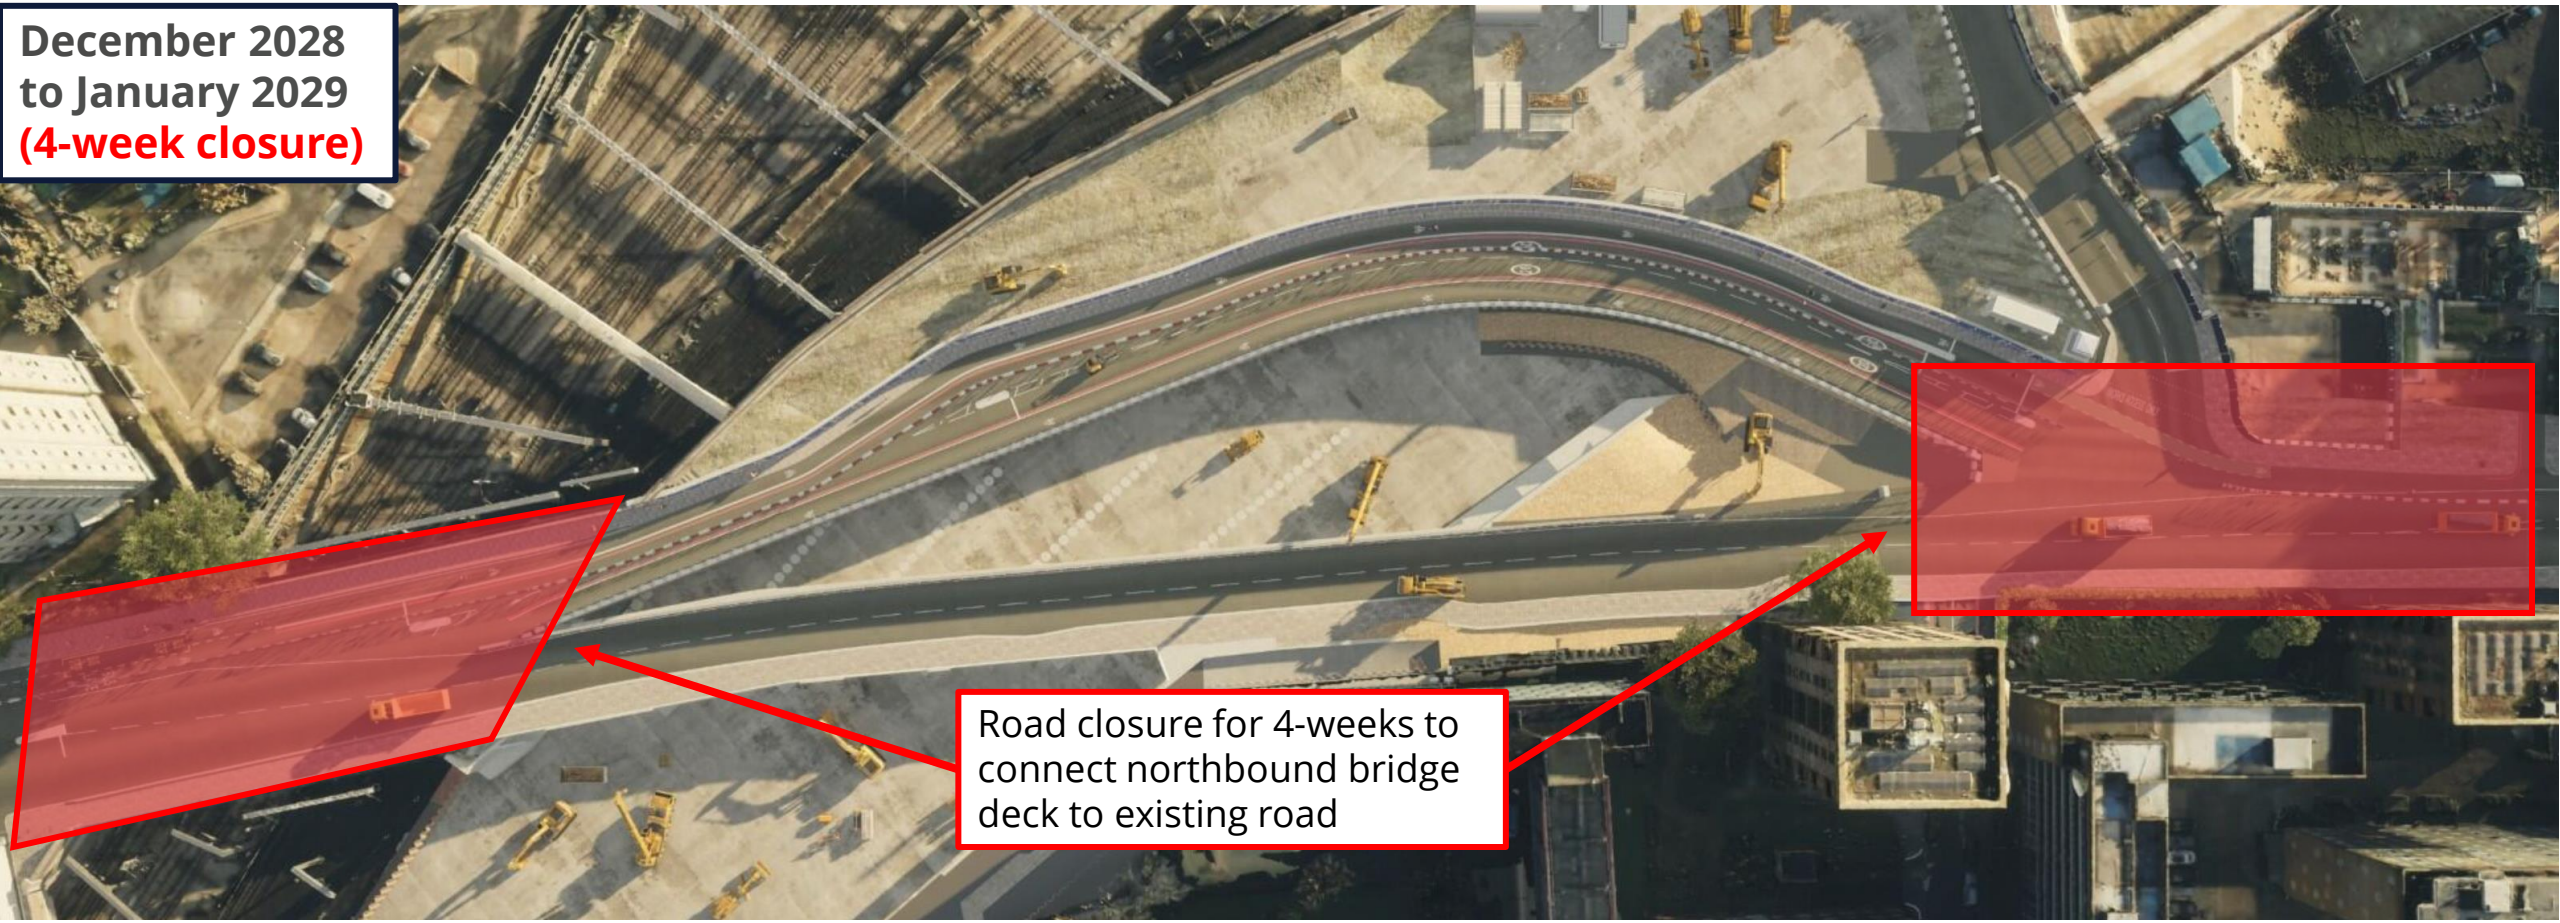


Hampstead Road bridge – Phase 5 – Temporary road removal

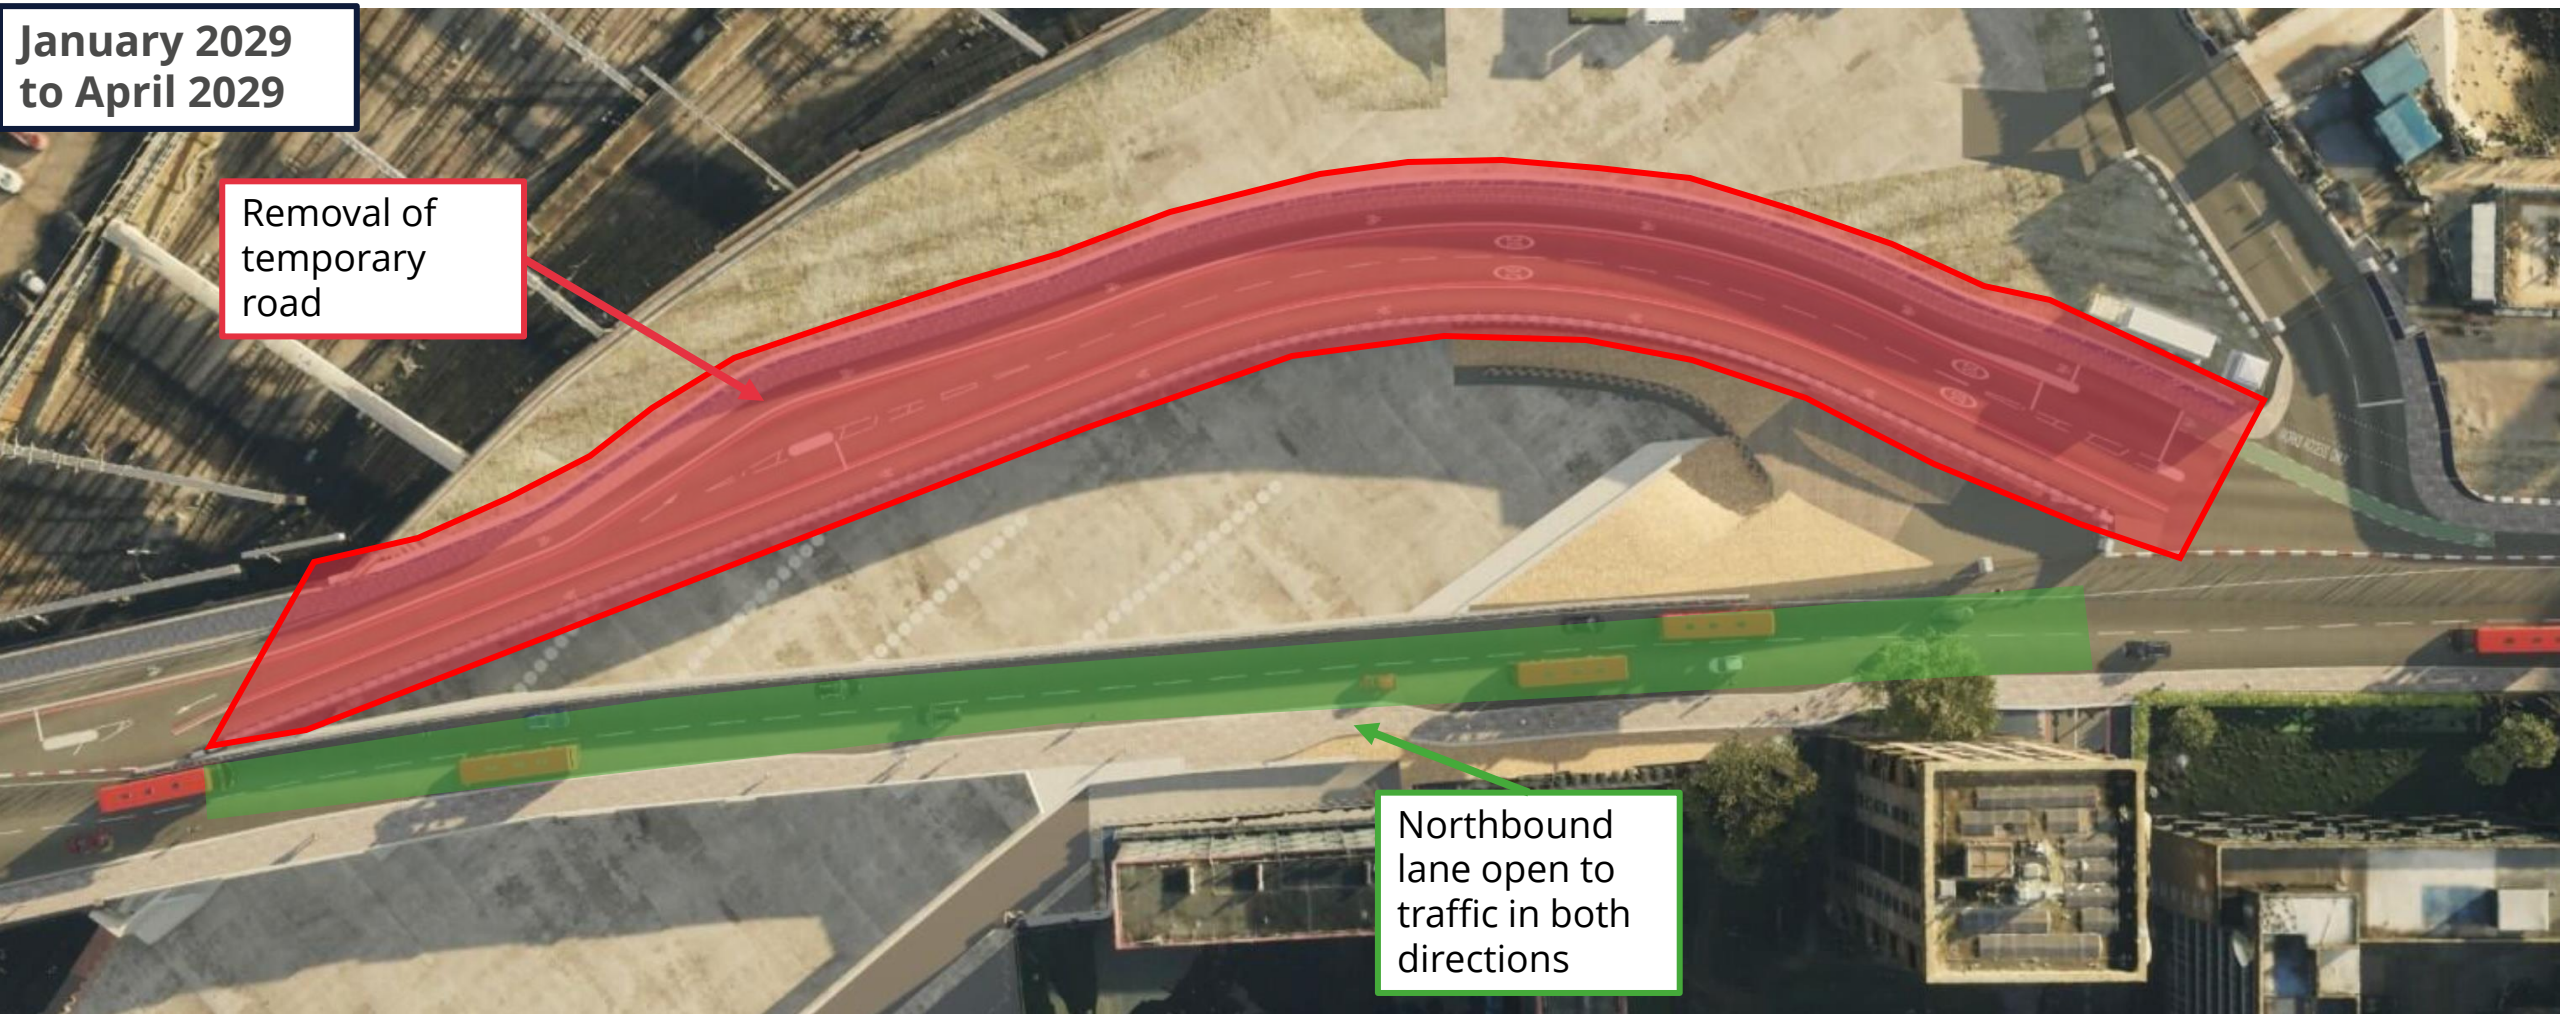

Hampstead Road bridge – Phase 6 – Southbound construction

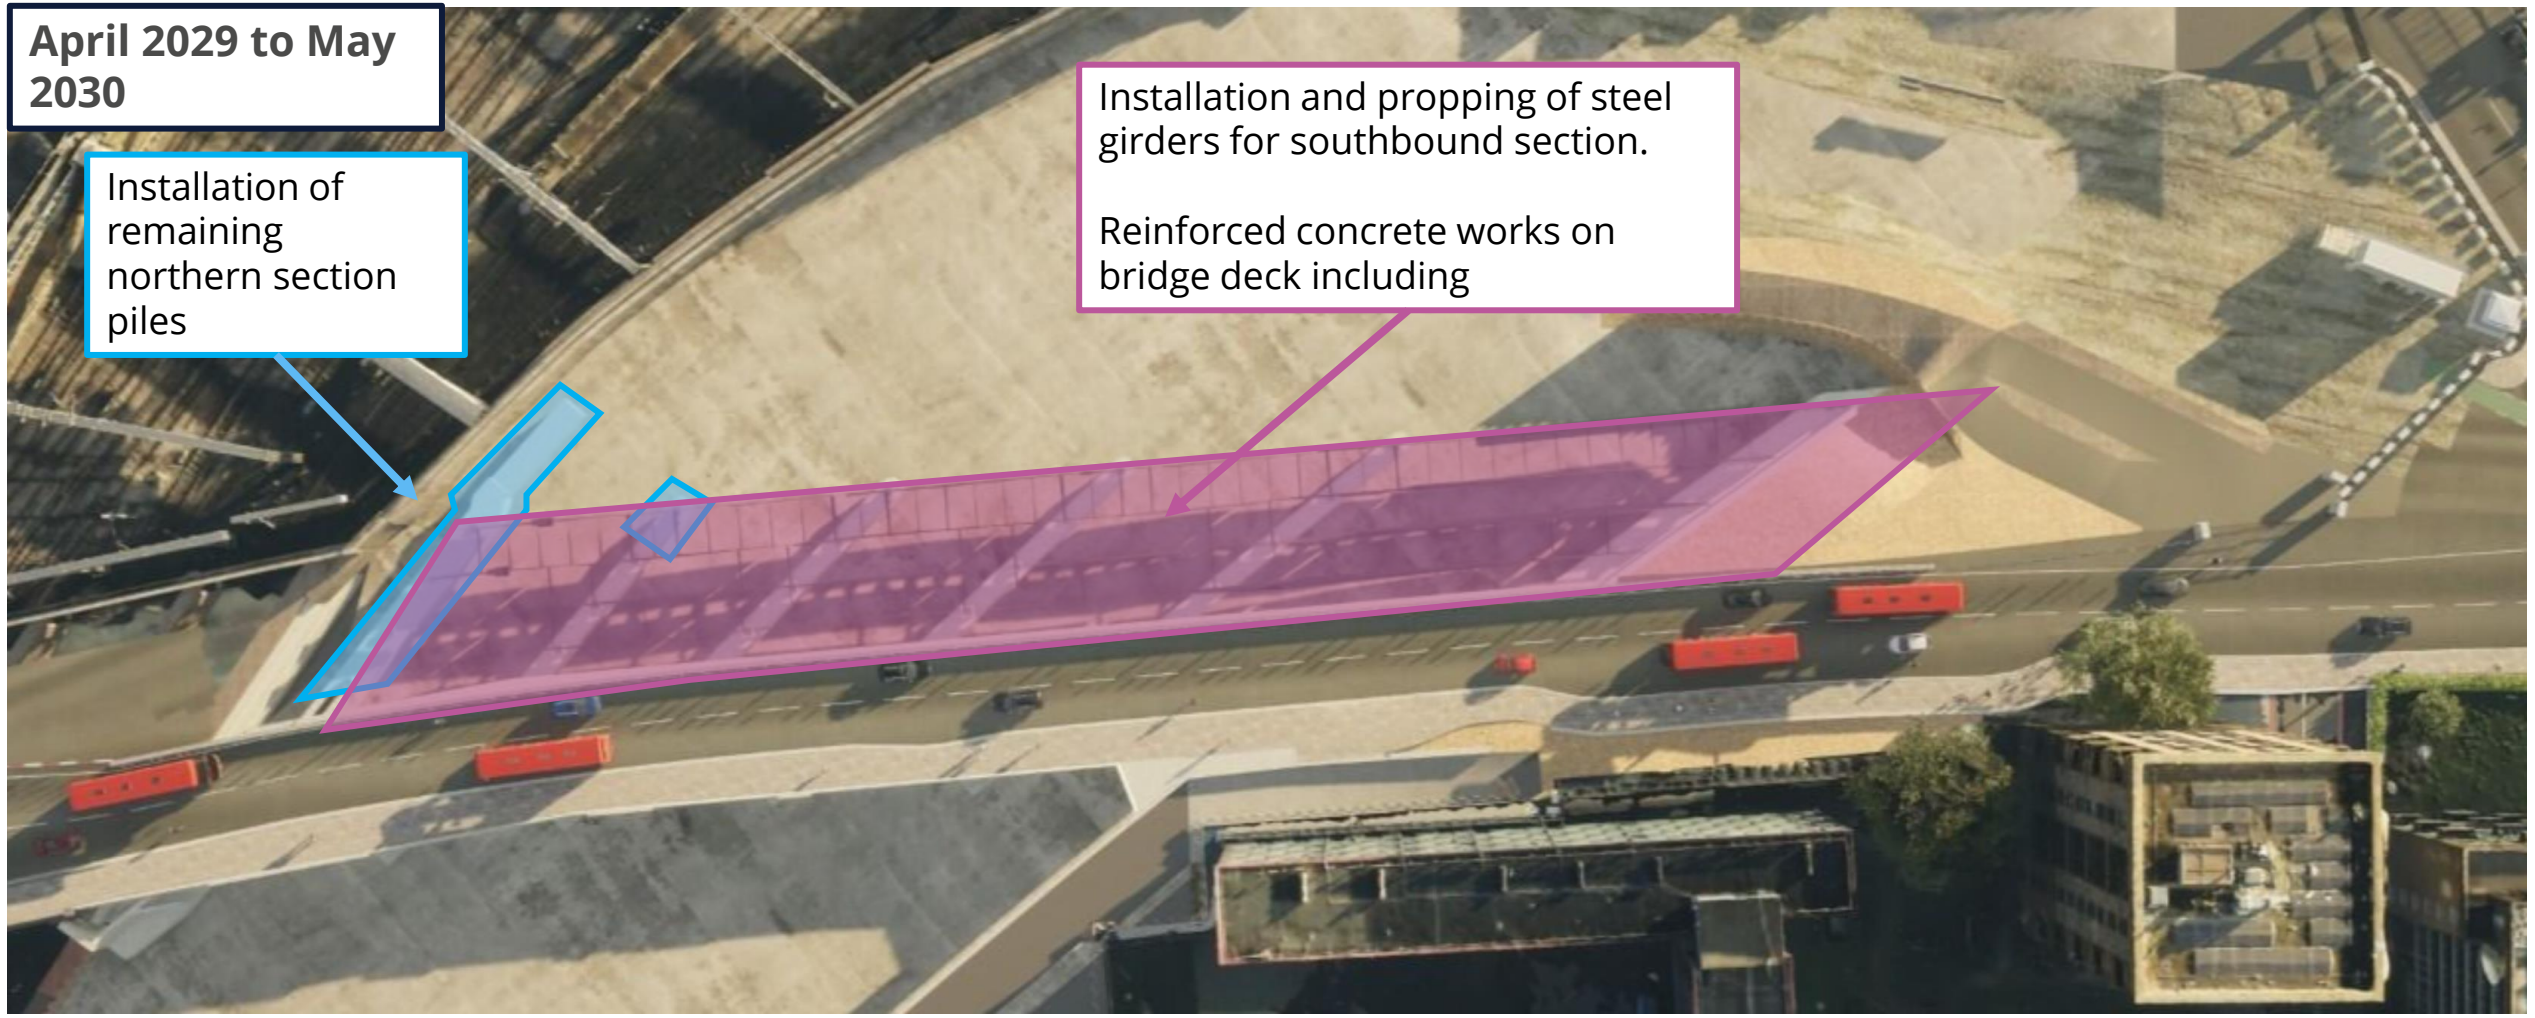


Hampstead Road bridge – Phase 7 – Connecting north and southbound bridge decks

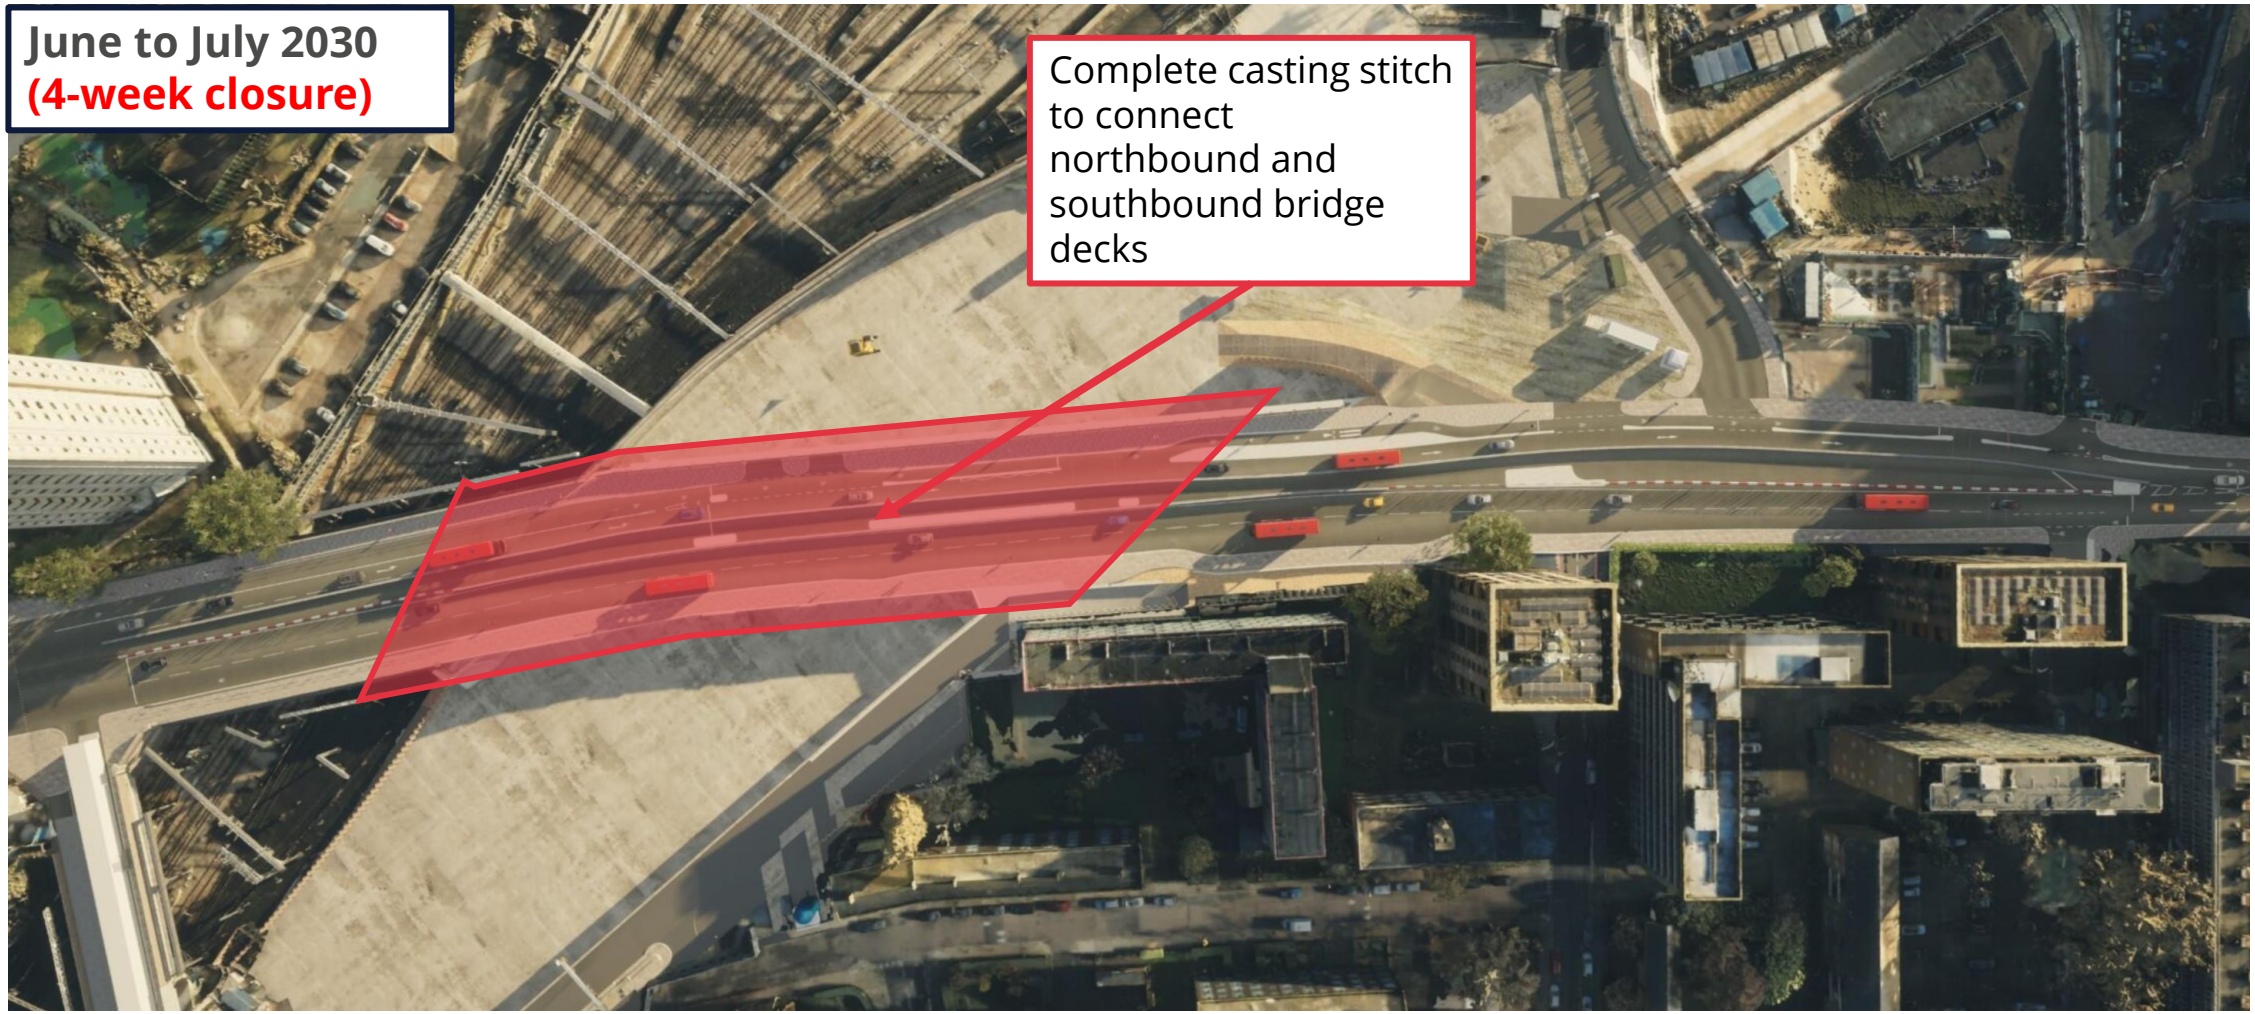

Hampstead Road bridge – Phase 8a – Base slab construction under the bridge



Hampstead Road bridge – Phase 8b – Finishing works

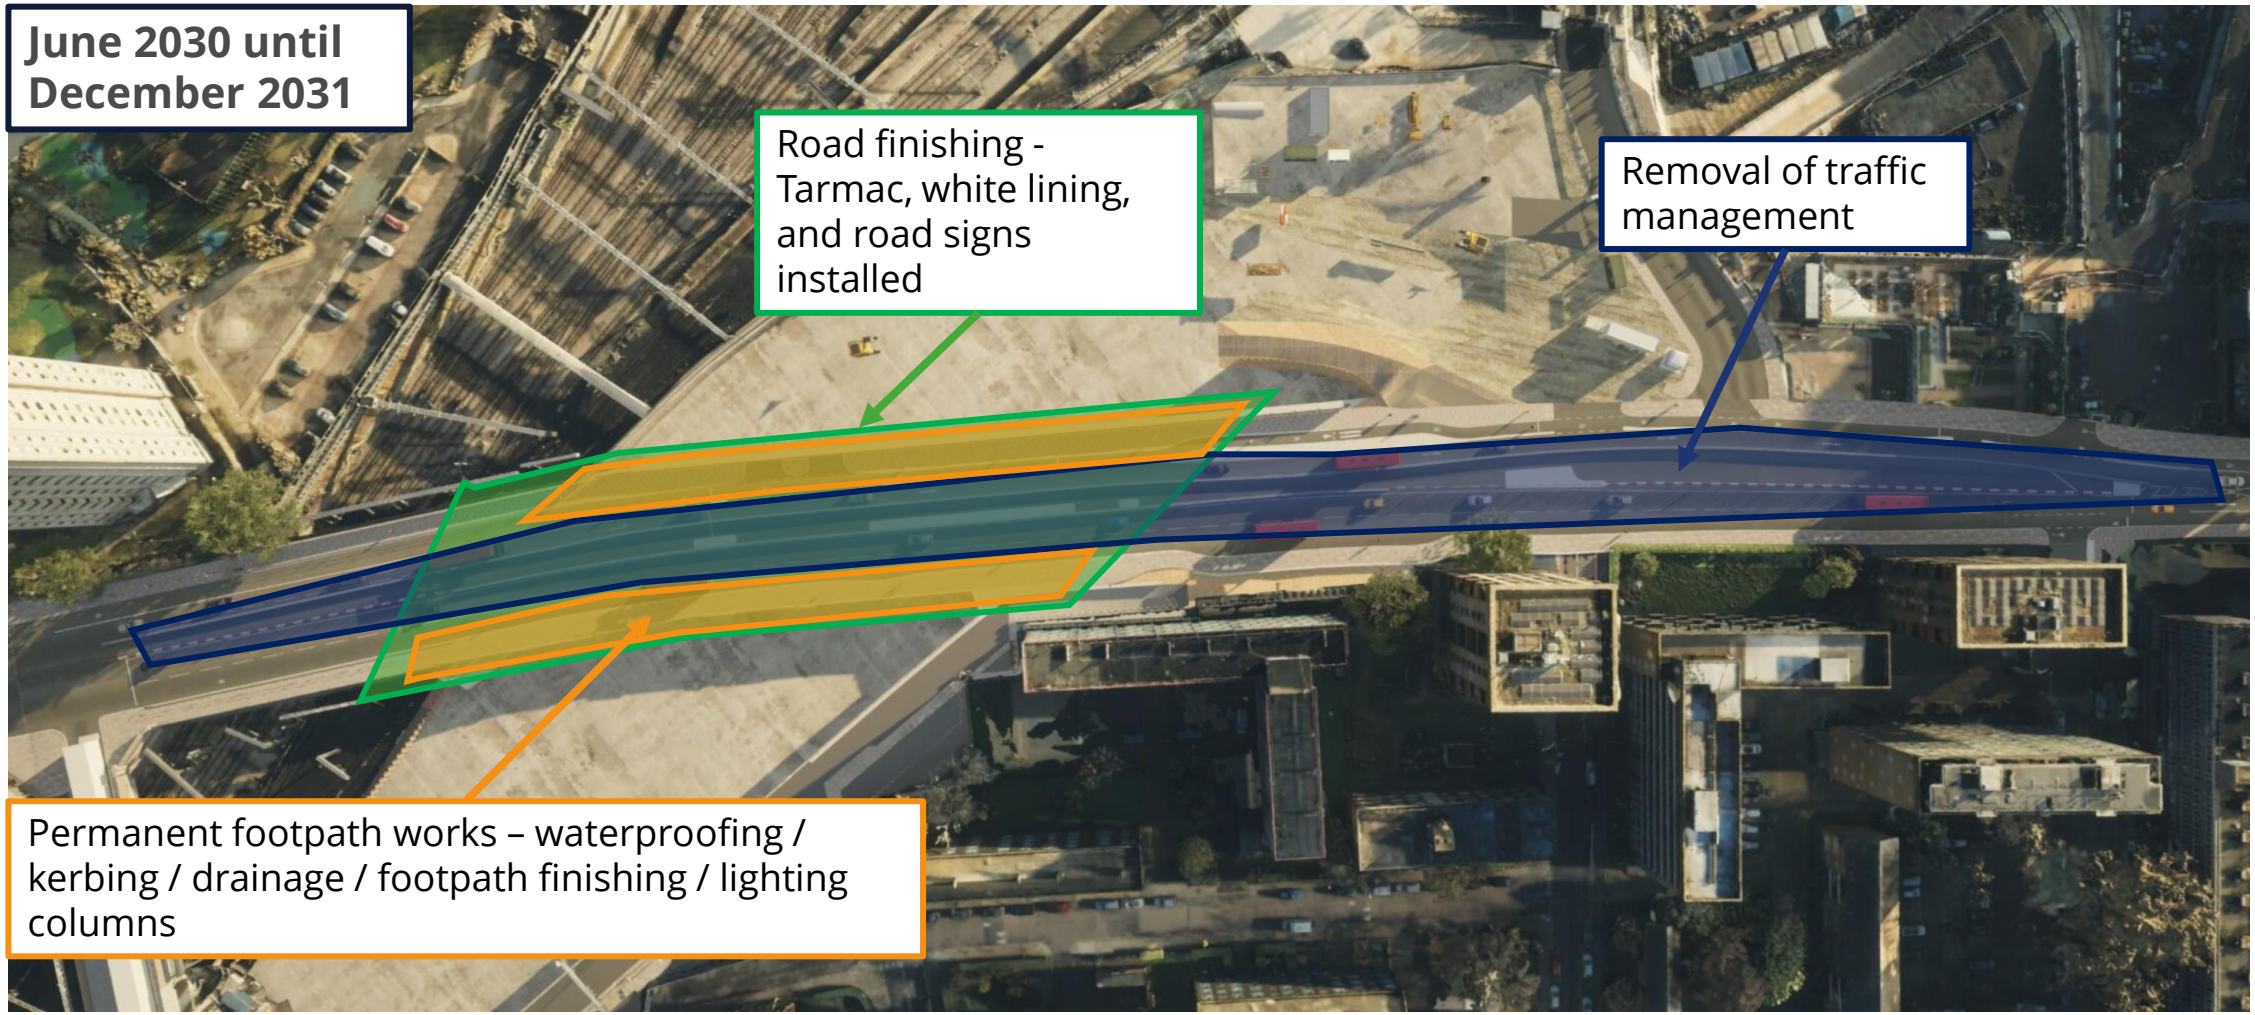

Text messaging service

We are launching a new SMS messaging service within the Euston Approaches to share information on our planned works, changes or delays to works, and extended working hours. We will also continue to engage with residents using our regular notices and information on the HS2 website. Each text message will contain a short summary of the key information and a link to the full update on the HS2 website.

Should you wish to receive our SMS updates please complete a short online form **here** by providing your name, contact number and street name. You will be able to unsubscribe at any time by following the link provided in each SMS.

Alternatively, you can sign up by scanning the QR code

HS2 helpdesk

For all enquiries, compliments or complaints please contact the HS2 helpdesk

- Freephone **08081 434 434**
- Email **HS2enquiries@hs2.org.uk**

We also encourage you to complete our **feedback form** to help us understand your concerns and ideas for making it easier to live next to major construction.

Scan the code with your phone's camera or QR code reader to open the form in a web page

You can sign up to receive updates about HS2 works in your local area at www.hs2inyourarea.co.uk

Thank you
