

SKANSKA



STRABAG

Working in
partnership with

HS2

Hampstead Road bridge construction

September 2026

Hampstead Road bridge construction

We need to extend Hampstead Road bridge to pass over the newly excavated and extended railway cutting. We'll build a temporary road to the east of Hampstead Road, over the area known as Zone 5 (see slide 5), to maintain an uninterrupted traffic flow on Hampstead Road while we extend the bridge. We expect these works to continue in phases until 2031.

We'll need to close Hampstead Road on three occasions for approximately four weeks each during this period. The first closure is currently scheduled for early 2027. We will update you on diversion routes closer to the time.

We understand these closures will impact the local community and we are looking at ways we can reduce the impacts, including durations of the road closures. We will confirm dates of the closures closer to the time.

We are holding events to engage with the local community about these works and understand their concerns.



Programme

Stage	Activity	Date
0	Mobilisation and site set up in Zone 5	June to October 2026
1	Temporary road construction, traffic switched to northbound lane	October 2026 to January 2027
2	First 4-week closure	January to February 2027
3	Temporary road in use, construction of northbound bridge deck	February 2027 to November 2028
4	Second 4-week closure , tie-in northbound carriageway to existing road	December 2028 to January 2029
5	Removal of temporary road, traffic on northbound bridge deck	January 2029 to June 2030
6	Southbound construction	April 2029 to May 2030
7	Third 4-week closure , bridge casting stitch	June to July 2030
8a	Base slab construction	July 2030 to December 2031
8b	Finishing works	June 2030 to December 2031



Keeping you informed

Regular engagement events


- Construction Update events – March and September
- Rooftop guided tour – March and September

Hampstead Road bridge focused engagement

- Drop-in events at the Euston Community Hub
- Regular notifications sent to local community


Text messaging service

- Should you wish to receive our SMS updates please complete a short online form by scanning the QR code above and providing your name, contact number and street name.

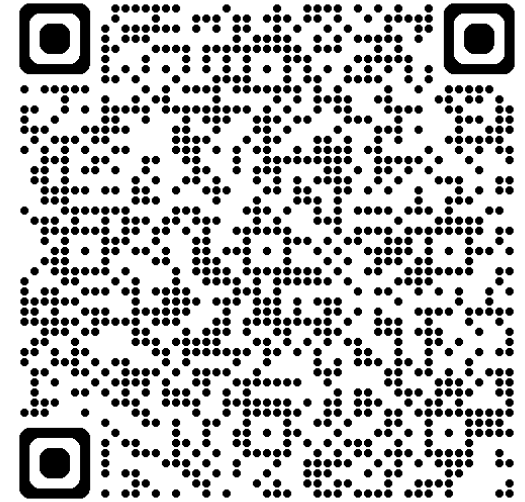


You can sign up to receive updates about HS2 works in your local area at
www.hs2inyourarea.co.uk


Hampstead Road Bridge – Stage 0 – Works inside Zone 5

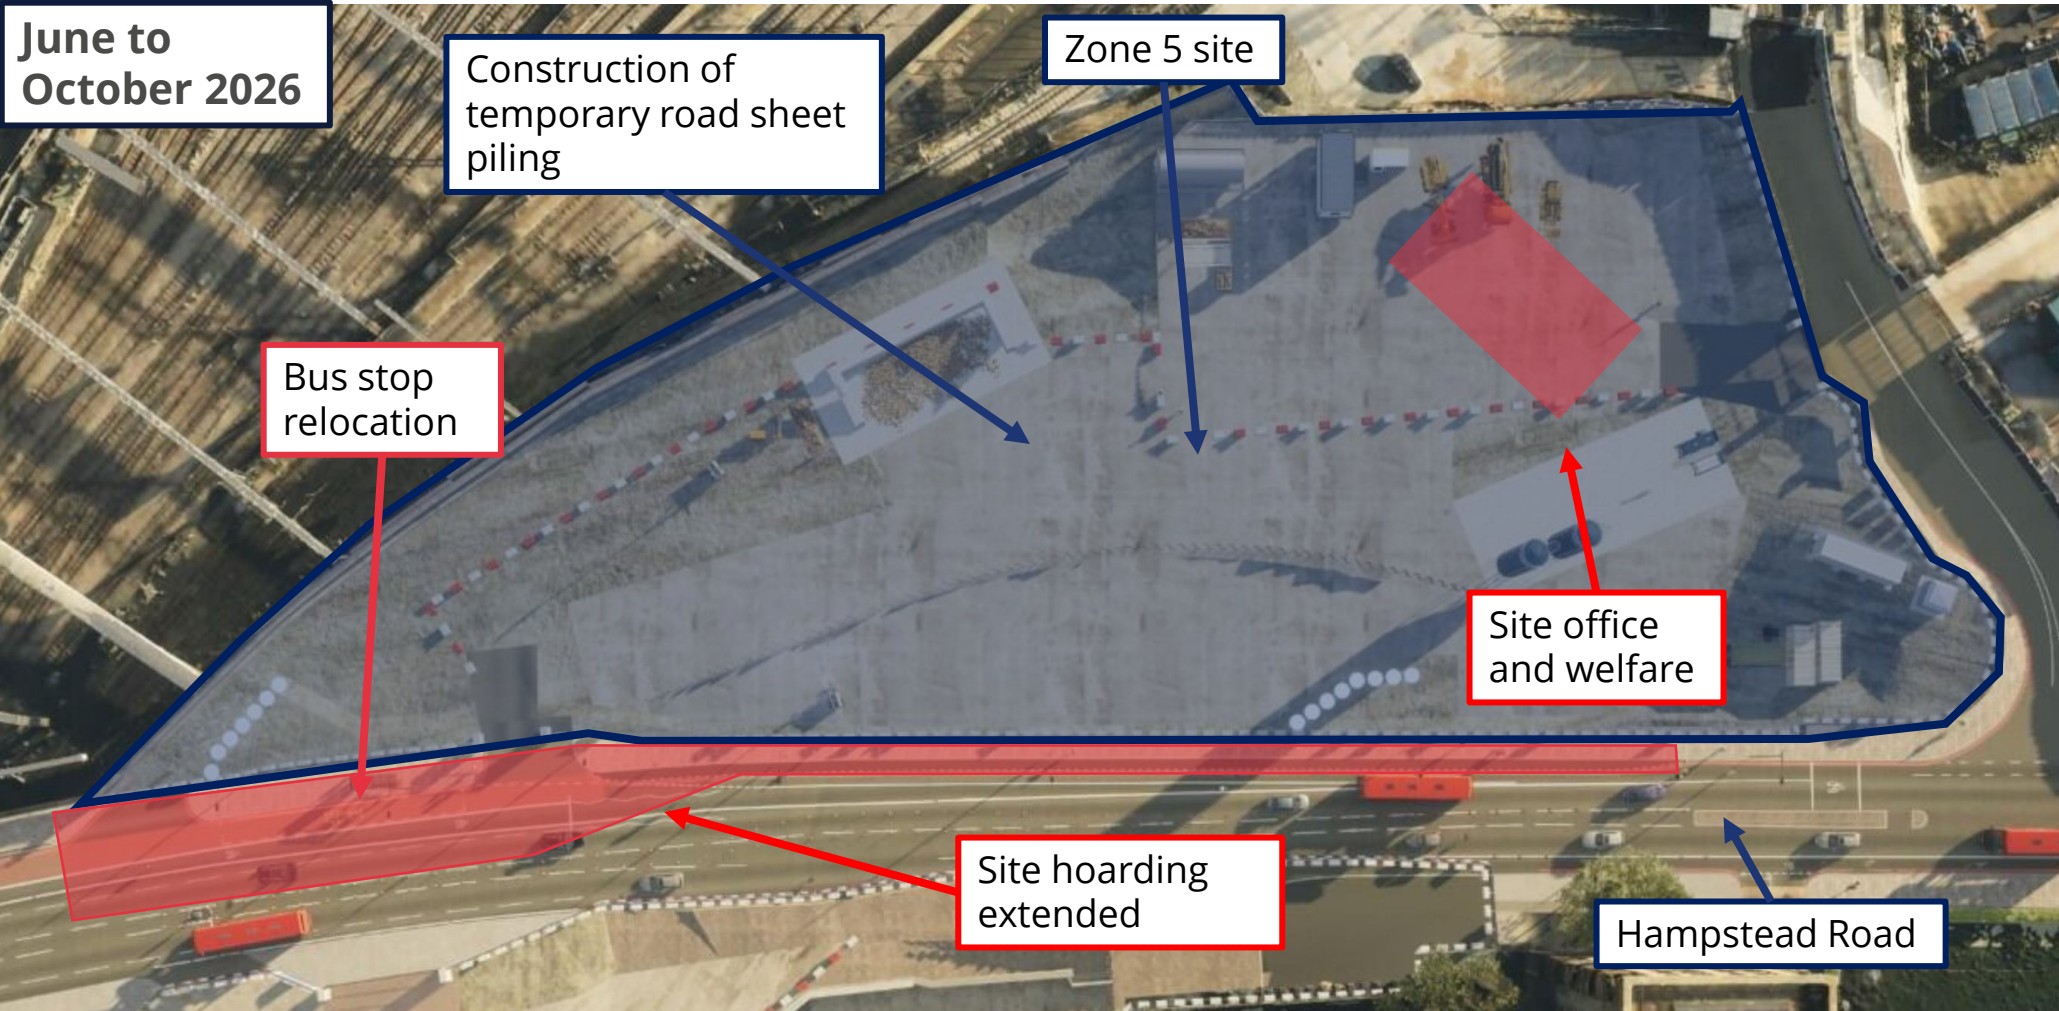

Hampstead Road Bridge – Stage 1 Road layout

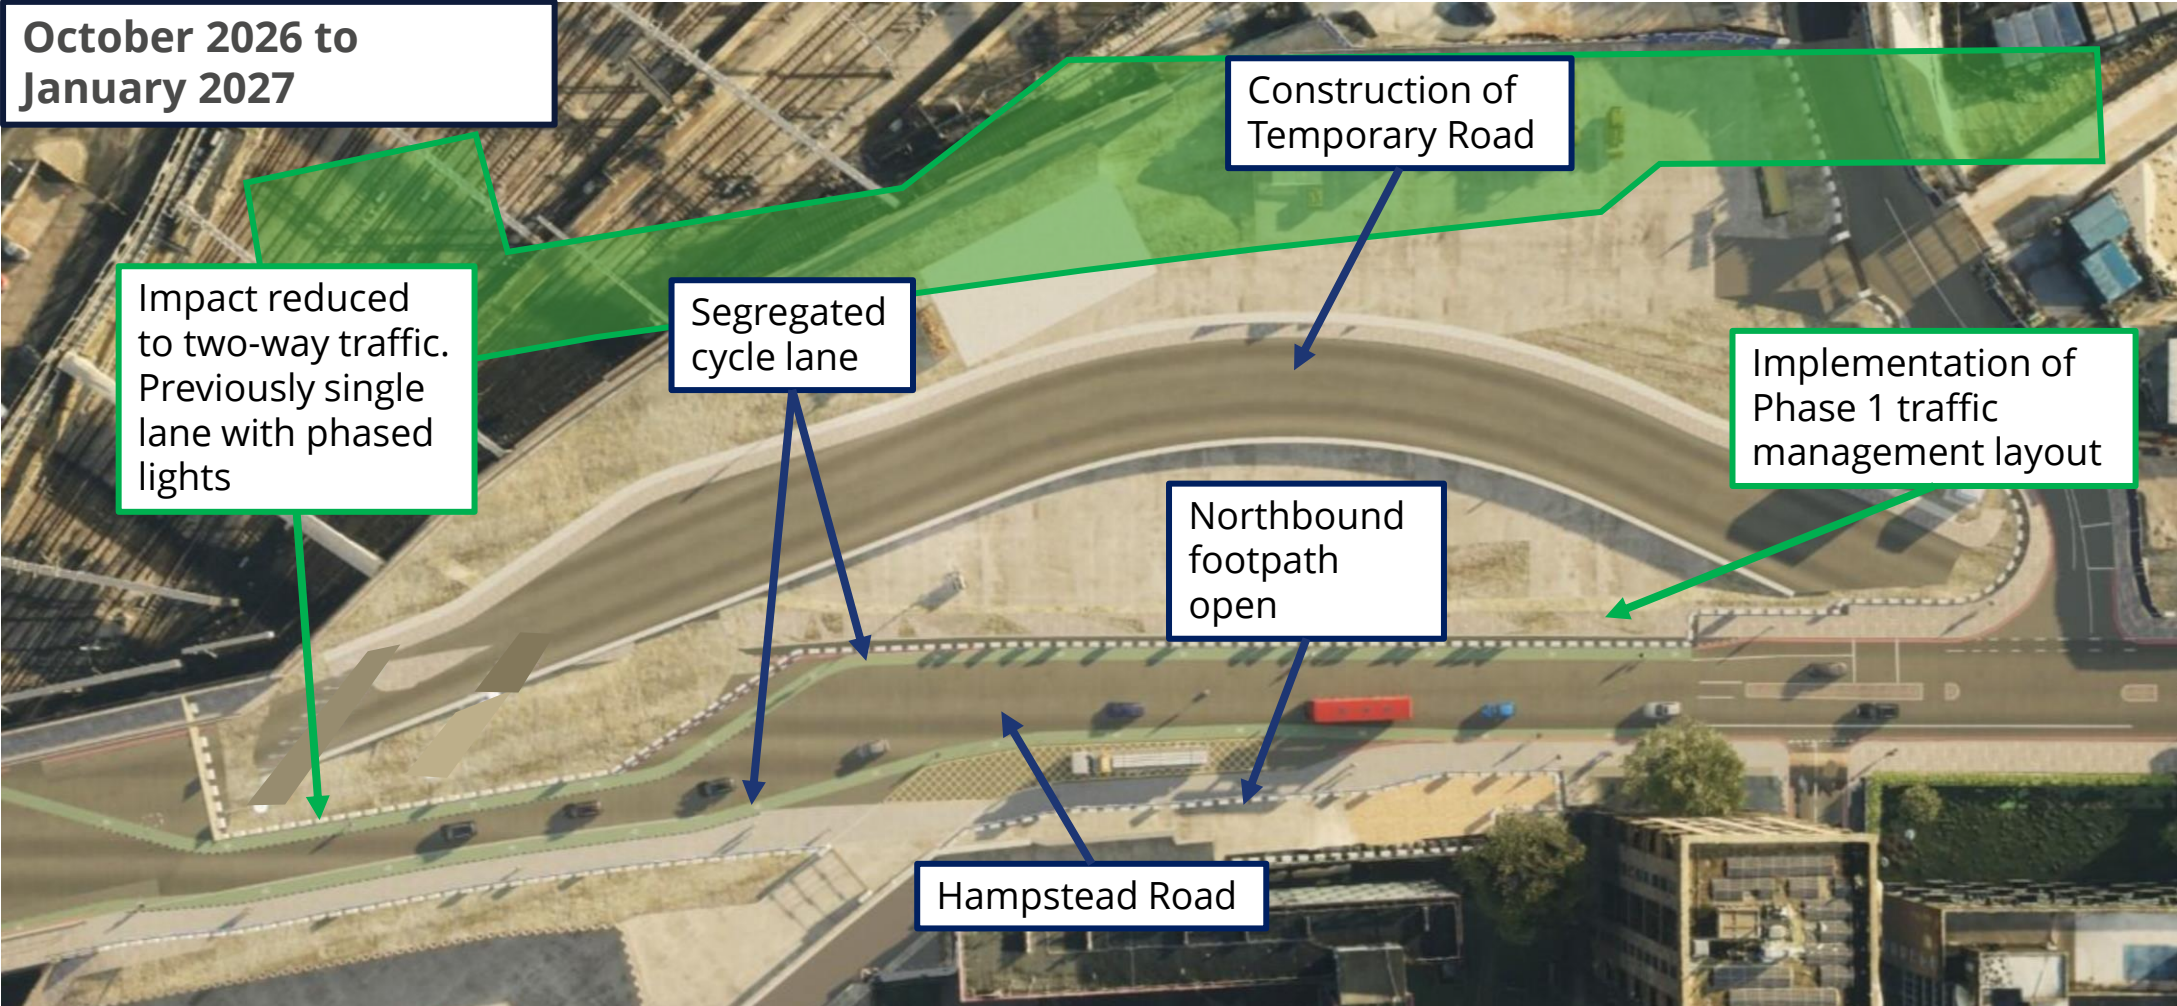


Hampstead Road Bridge – Stage 1 Traffic Management - Northbound

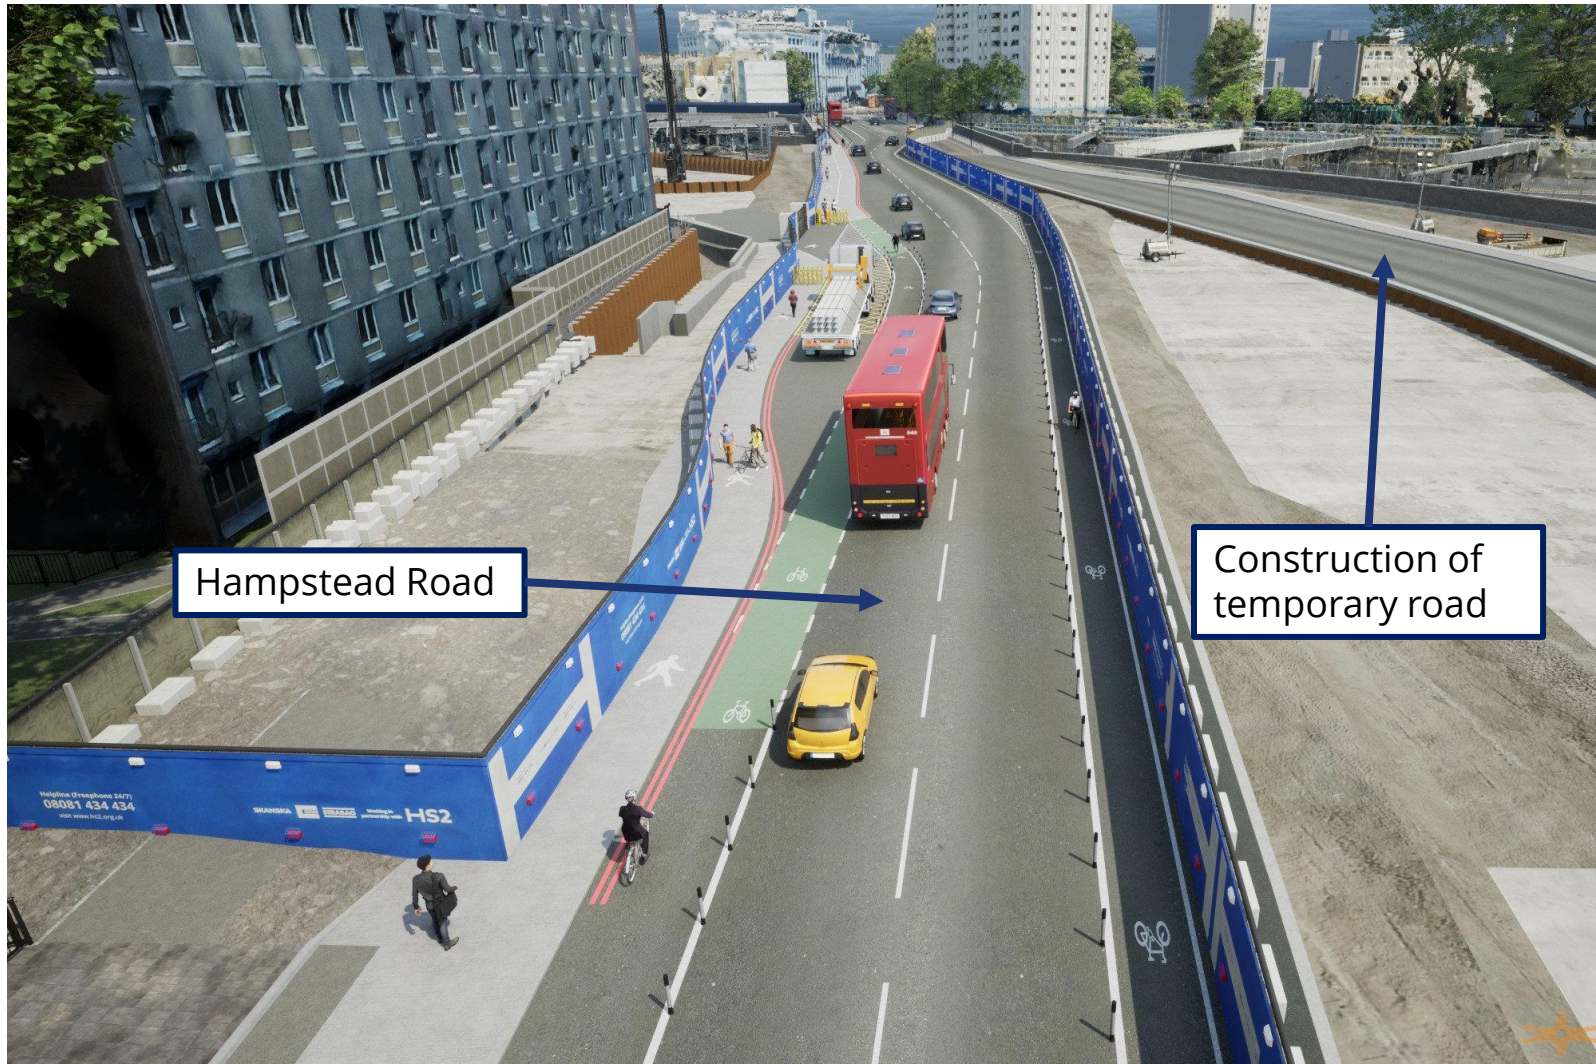

- Traffic maintained in both directions
- Pedestrians to use northbound footpath
- Segregated cycle lane in both directions

Hampstead Road Bridge – Stage 1 Traffic Management - Southbound

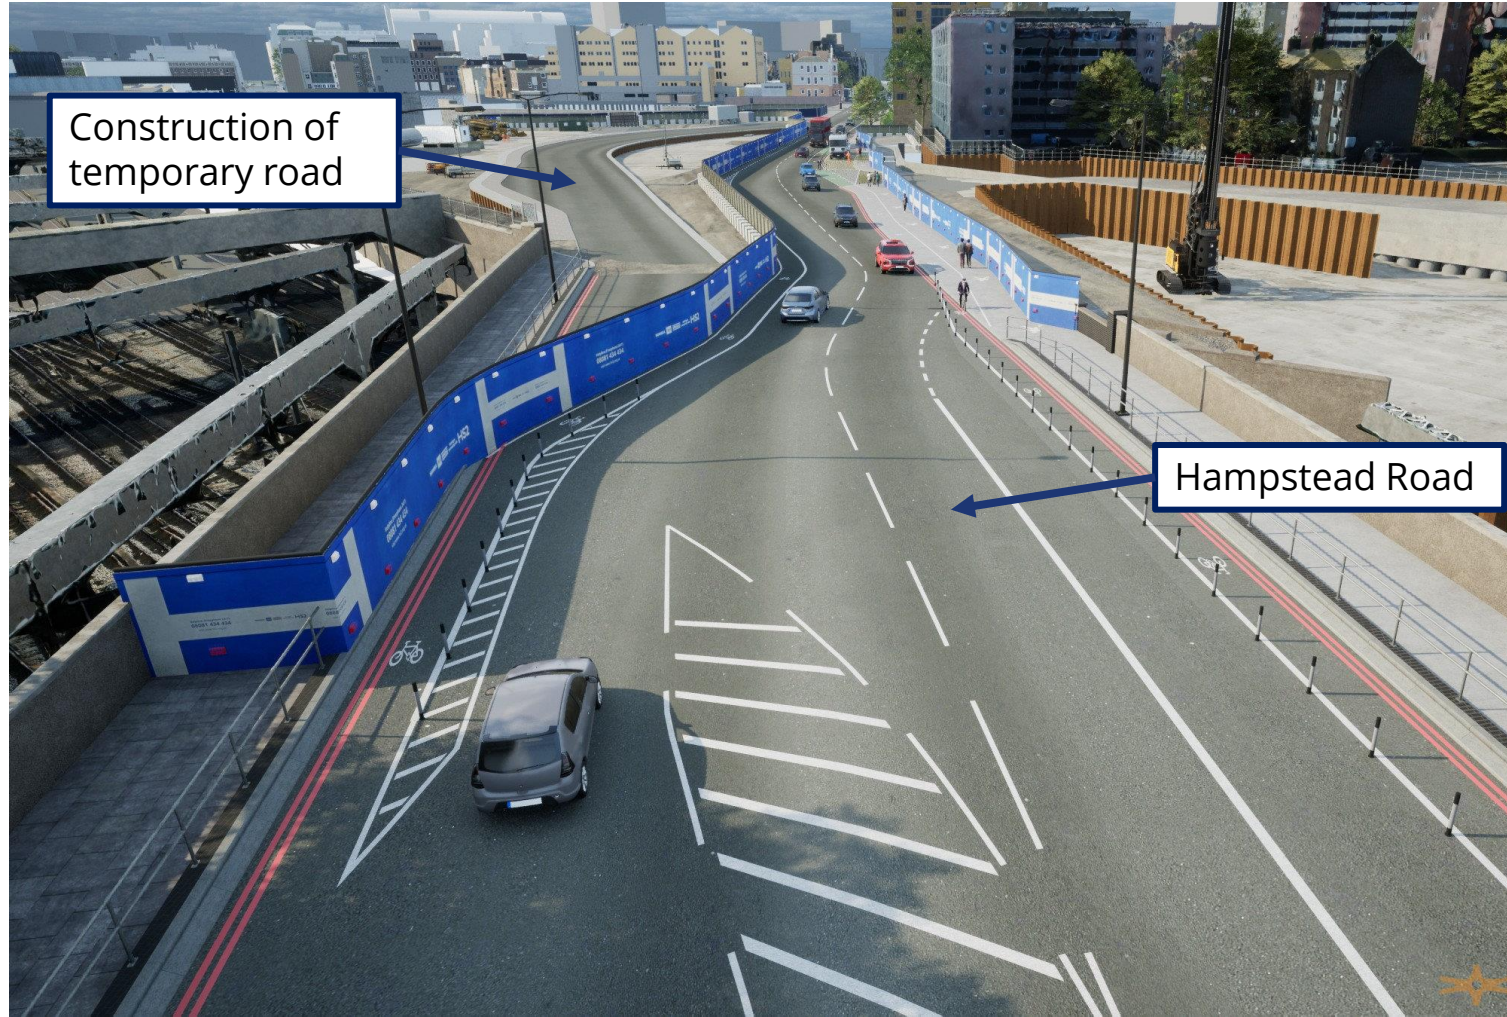


- Traffic maintained in both directions
- Pedestrians to use northbound footpath
- Segregated cycle lane in both directions
- Bus stop W relocated 80m north, closer to Amptill Estate

Hampstead Road Bridge – Stage 2 – Road Closure for Temporary Road connection works


January to February
2027 (4-week closure)

Works to connect
temporary road to existing
road, install remaining
traffic lights and install
footpath

Working areas during
4-week closure

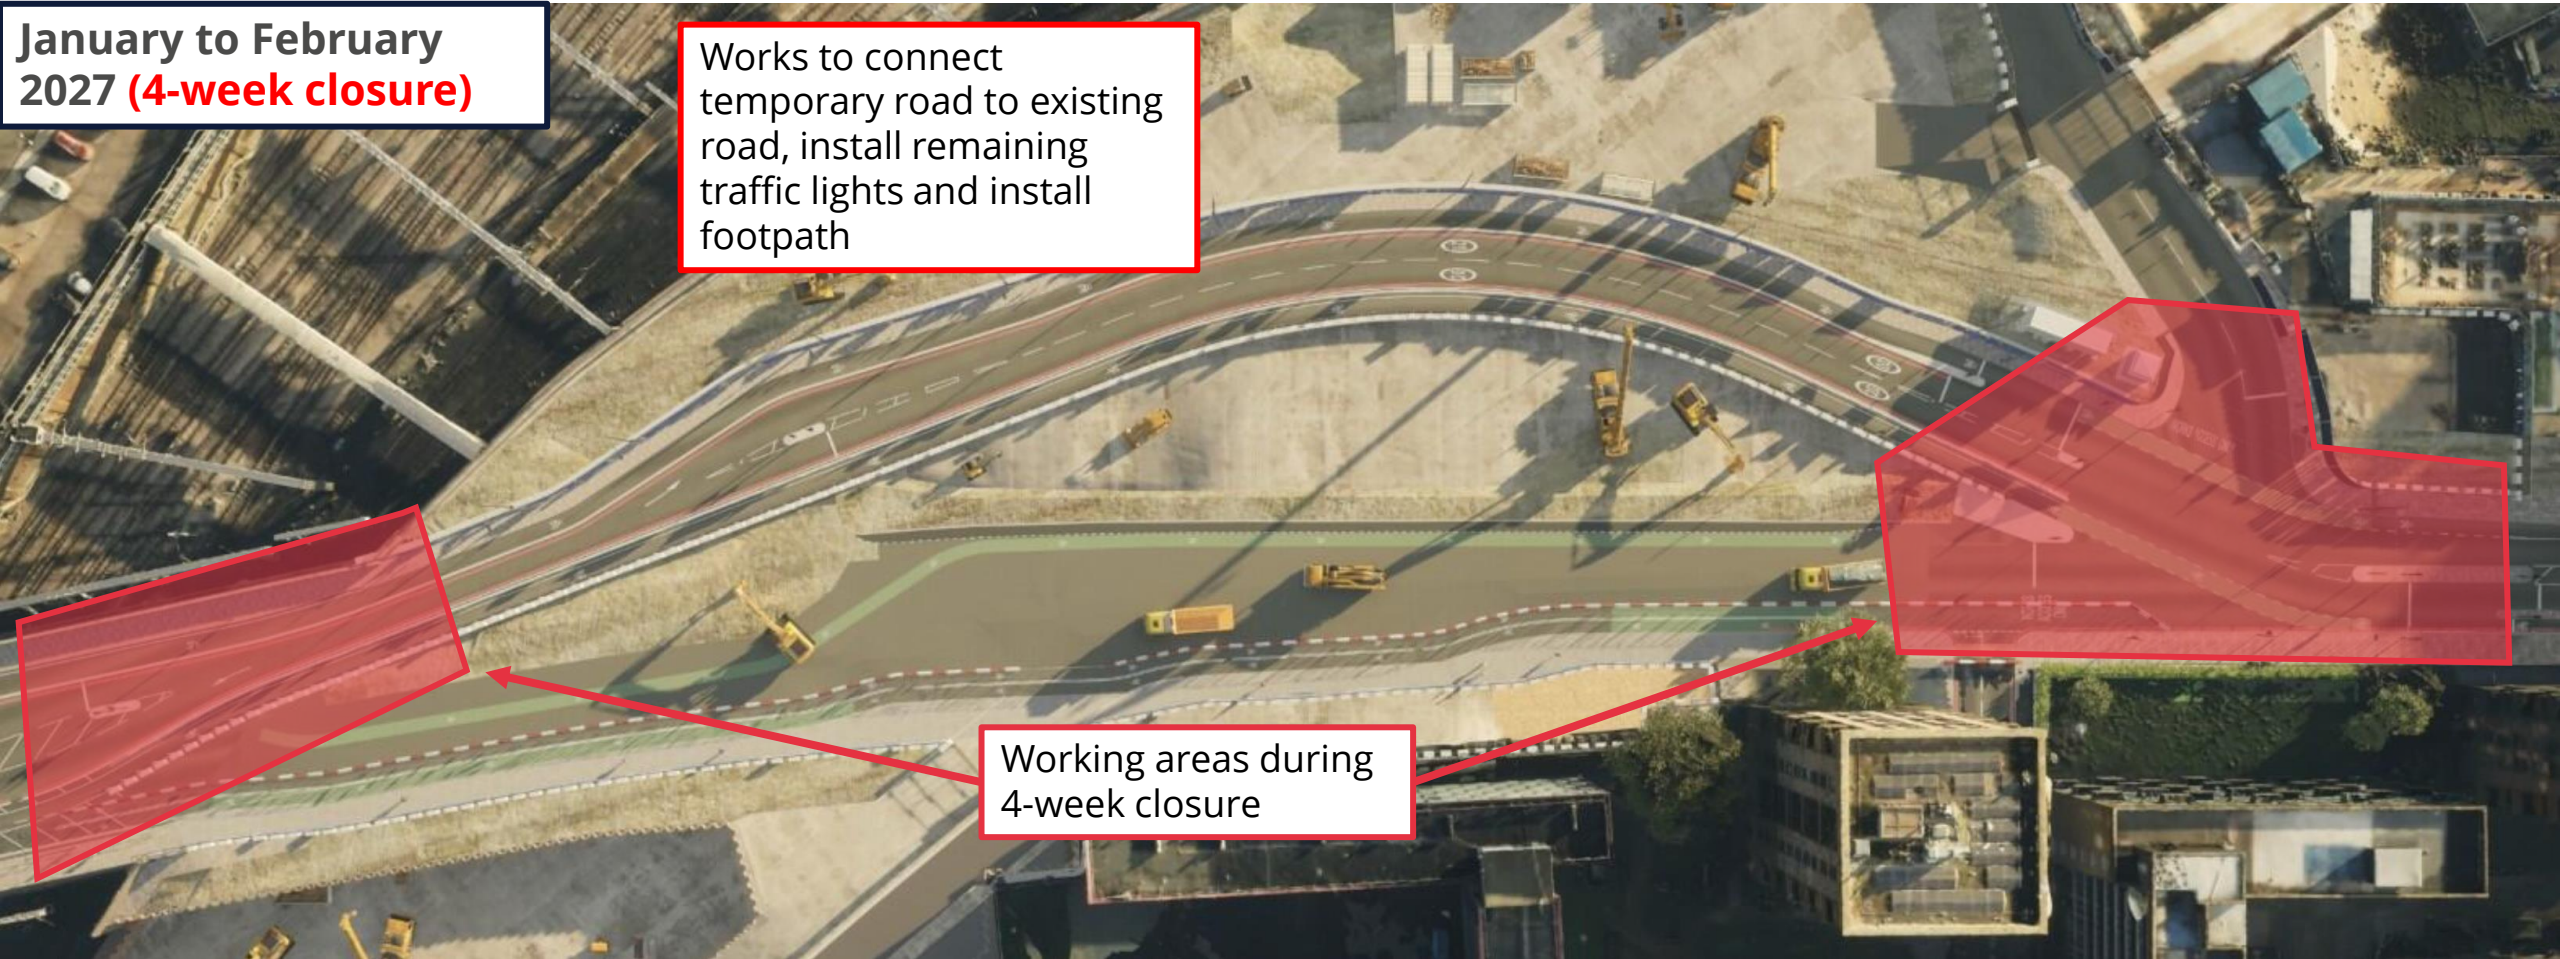


Hampstead Road Bridge – Stage 3 – Temporary Road in use

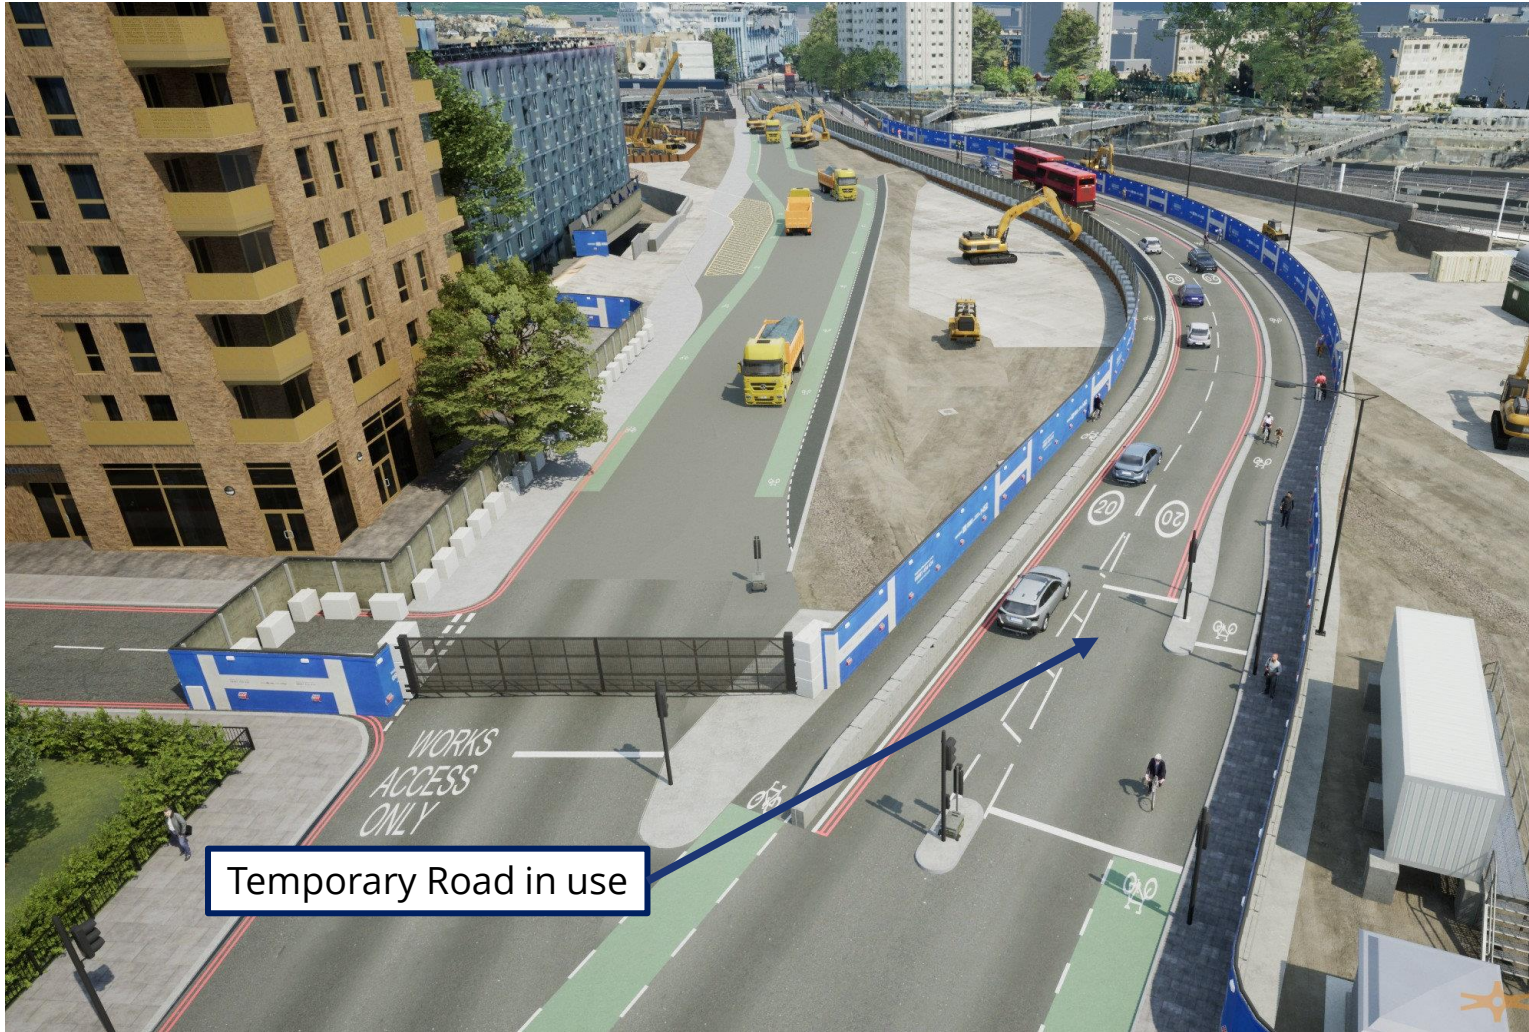


- Traffic maintained in both directions
- Pedestrians to use southbound footpath
- Segregated cycle lane in both directions

Hampstead Road Bridge – Stage 3 – Temporary Road in use

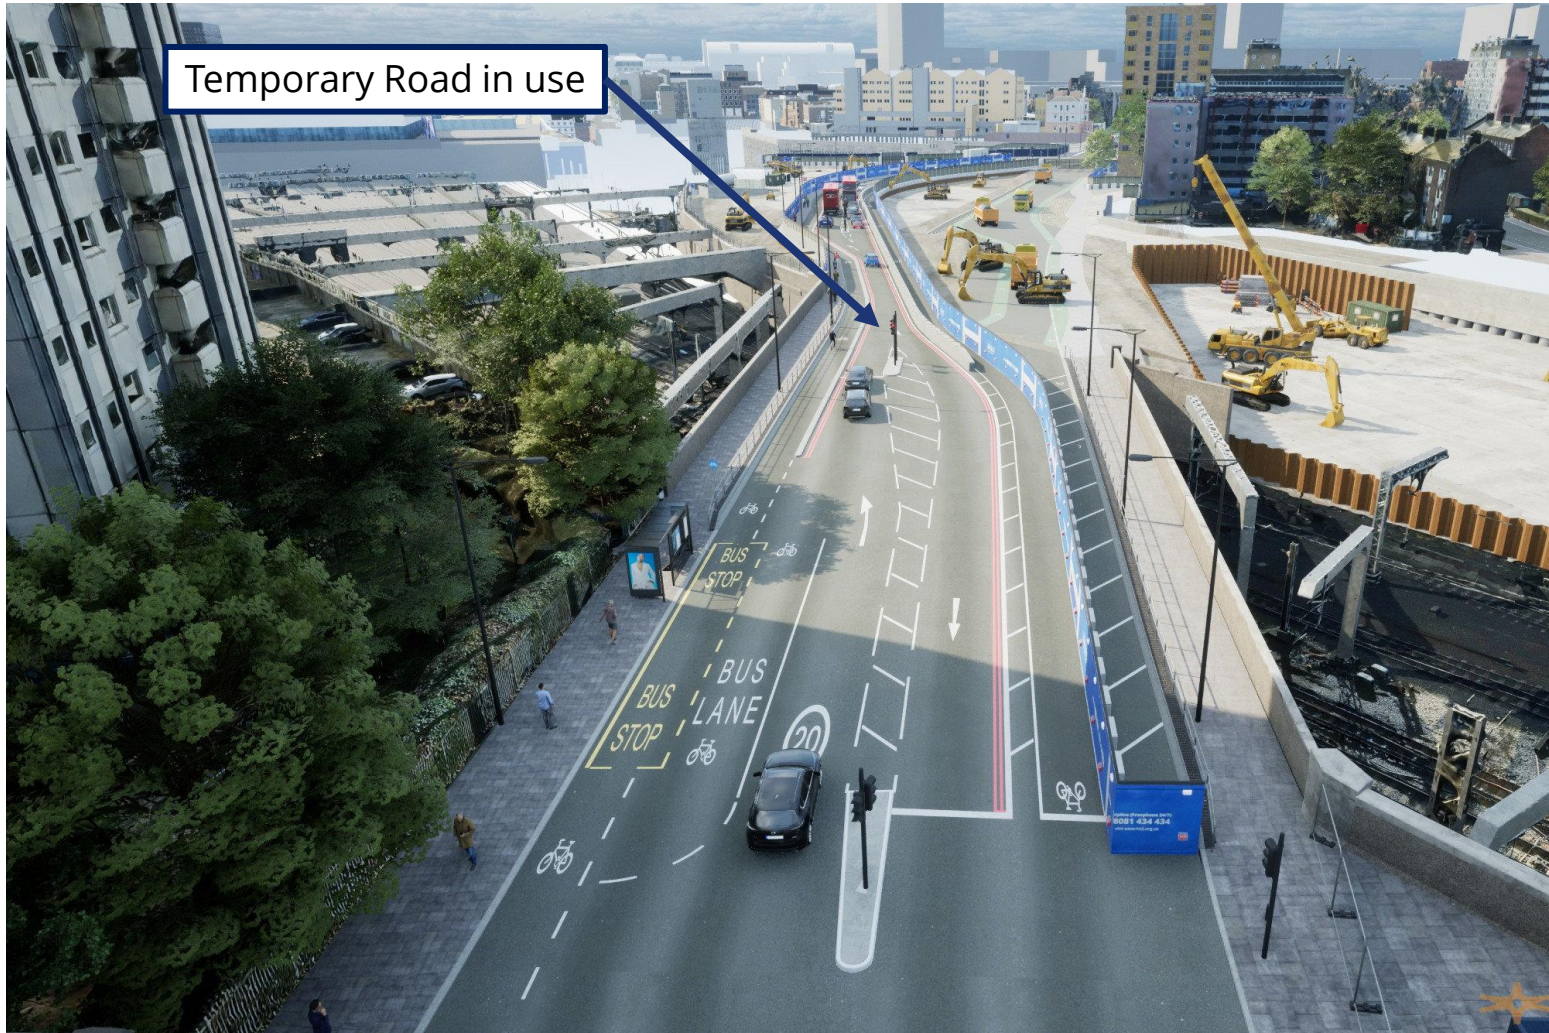

- Traffic maintained in both directions
- Pedestrians to use southbound footpath
- Segregated cycle lane in both directions

Hampstead Road Bridge – Stage 3 – Construction of Northbound Bridge Deck

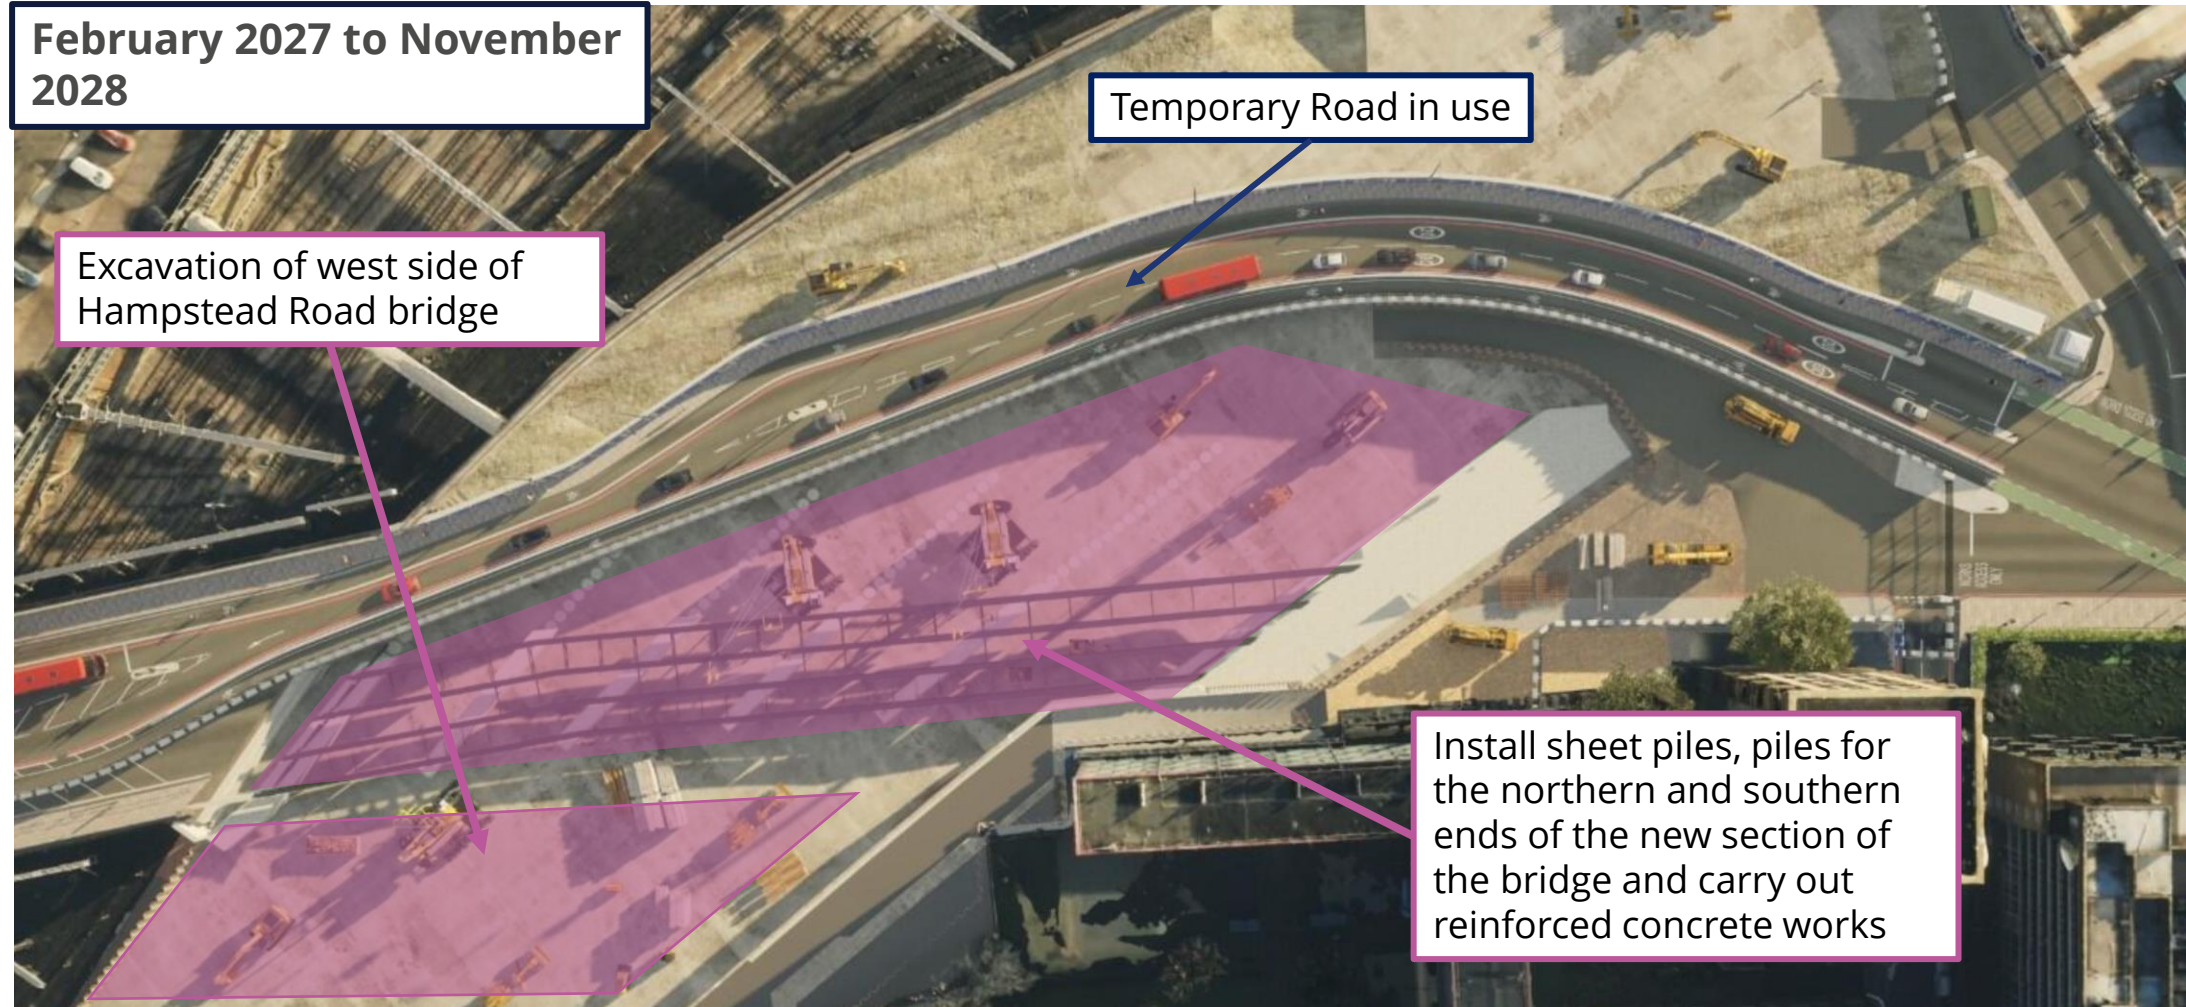

Stage 3 – Northbound Deck Construction



Hampstead Road Bridge – Stage 3 – Construction of Northbound Bridge Deck


February to
November 2028

Finishing works to northbound bridge deck including works to drainage, lighting and kerbing



Hampstead Road Bridge – Stage 4 – Northbound Tie in. Traffic Moves to Northbound lane

December 2028
to January 2029
(4-week closure)

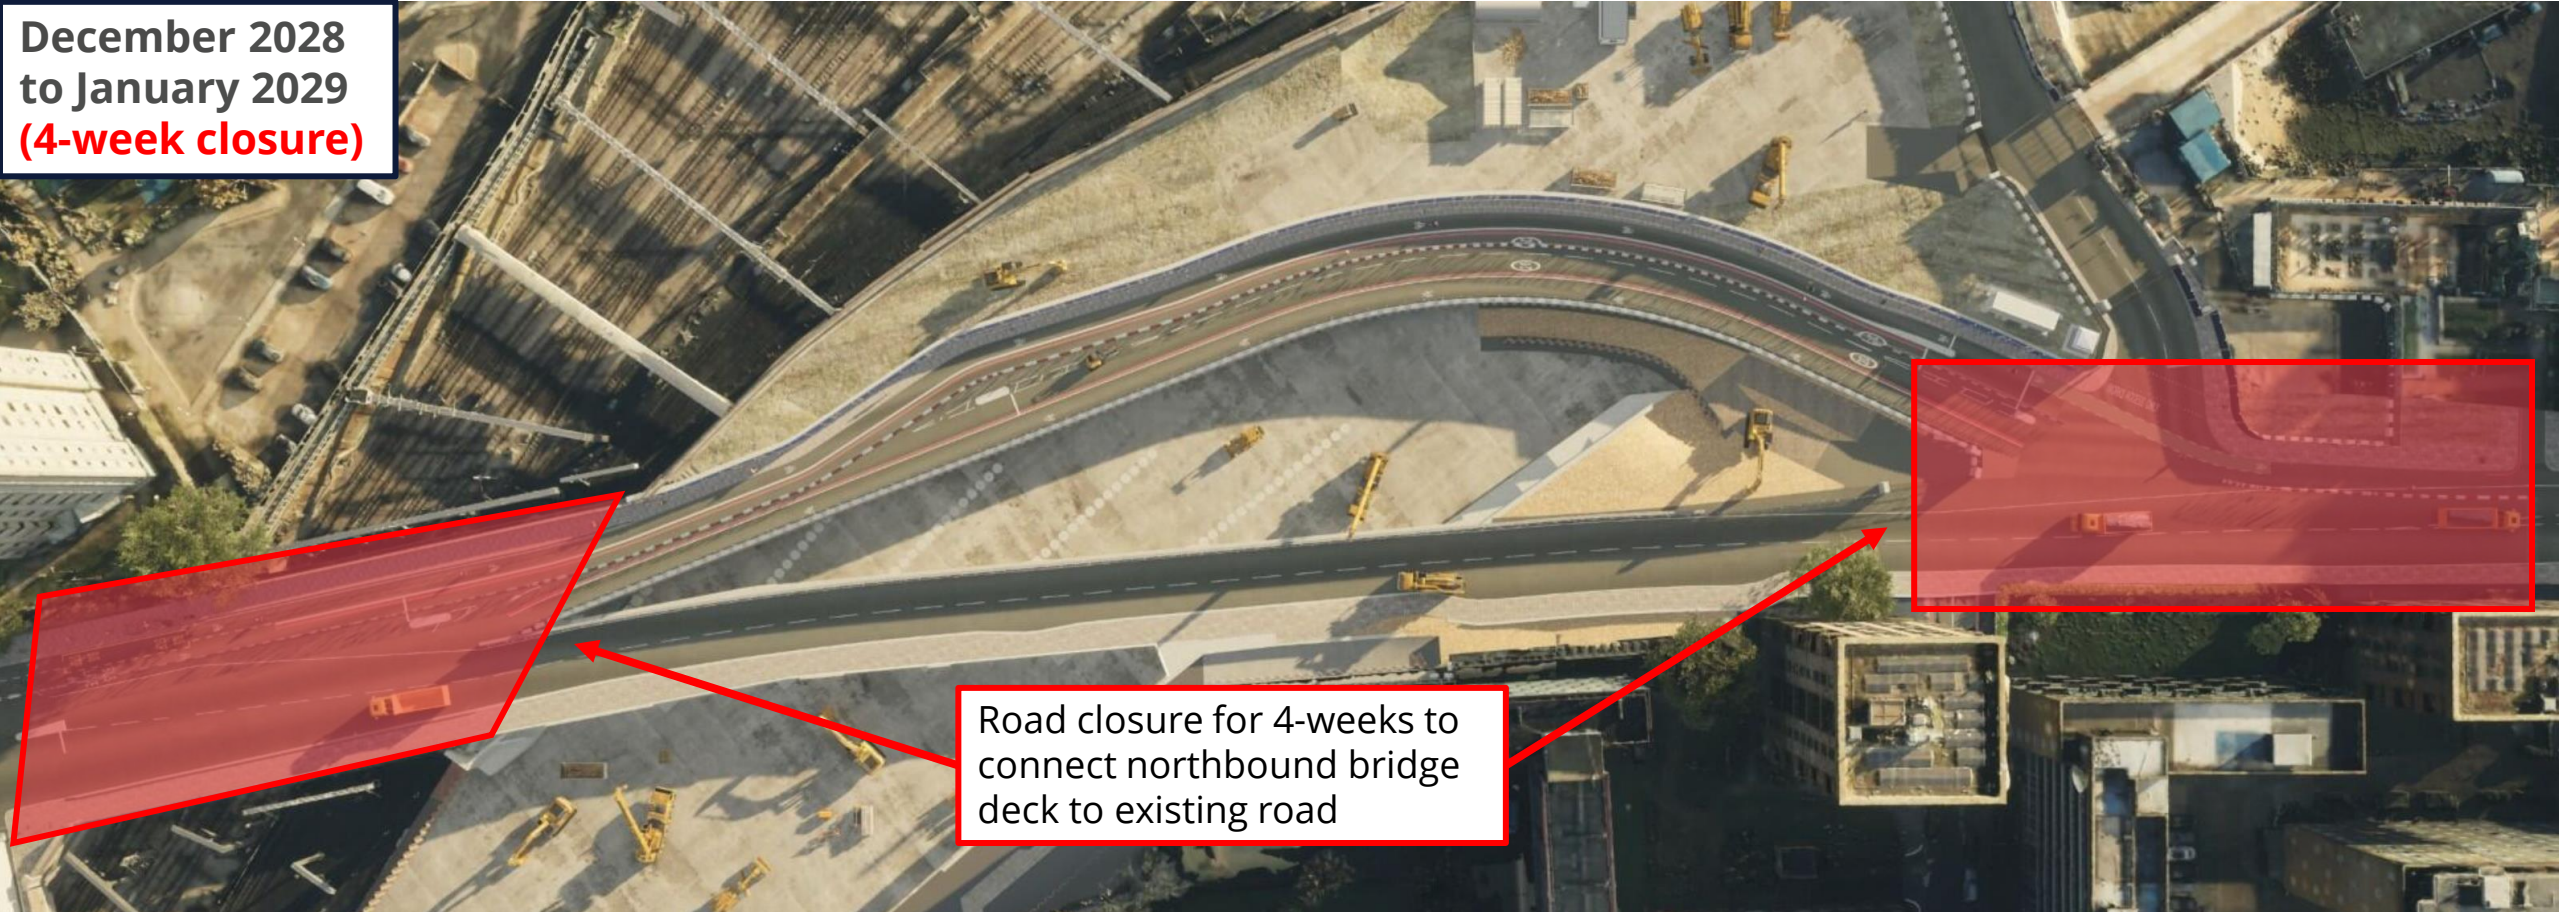


Road closure for 4-weeks to
connect northbound bridge
deck to existing road

Hampstead Road Bridge – Stage 5 – Temporary Road removal

January 2029 to June 2030

Removal of
temporary
road

Northbound
lane open to
traffic in both
directions

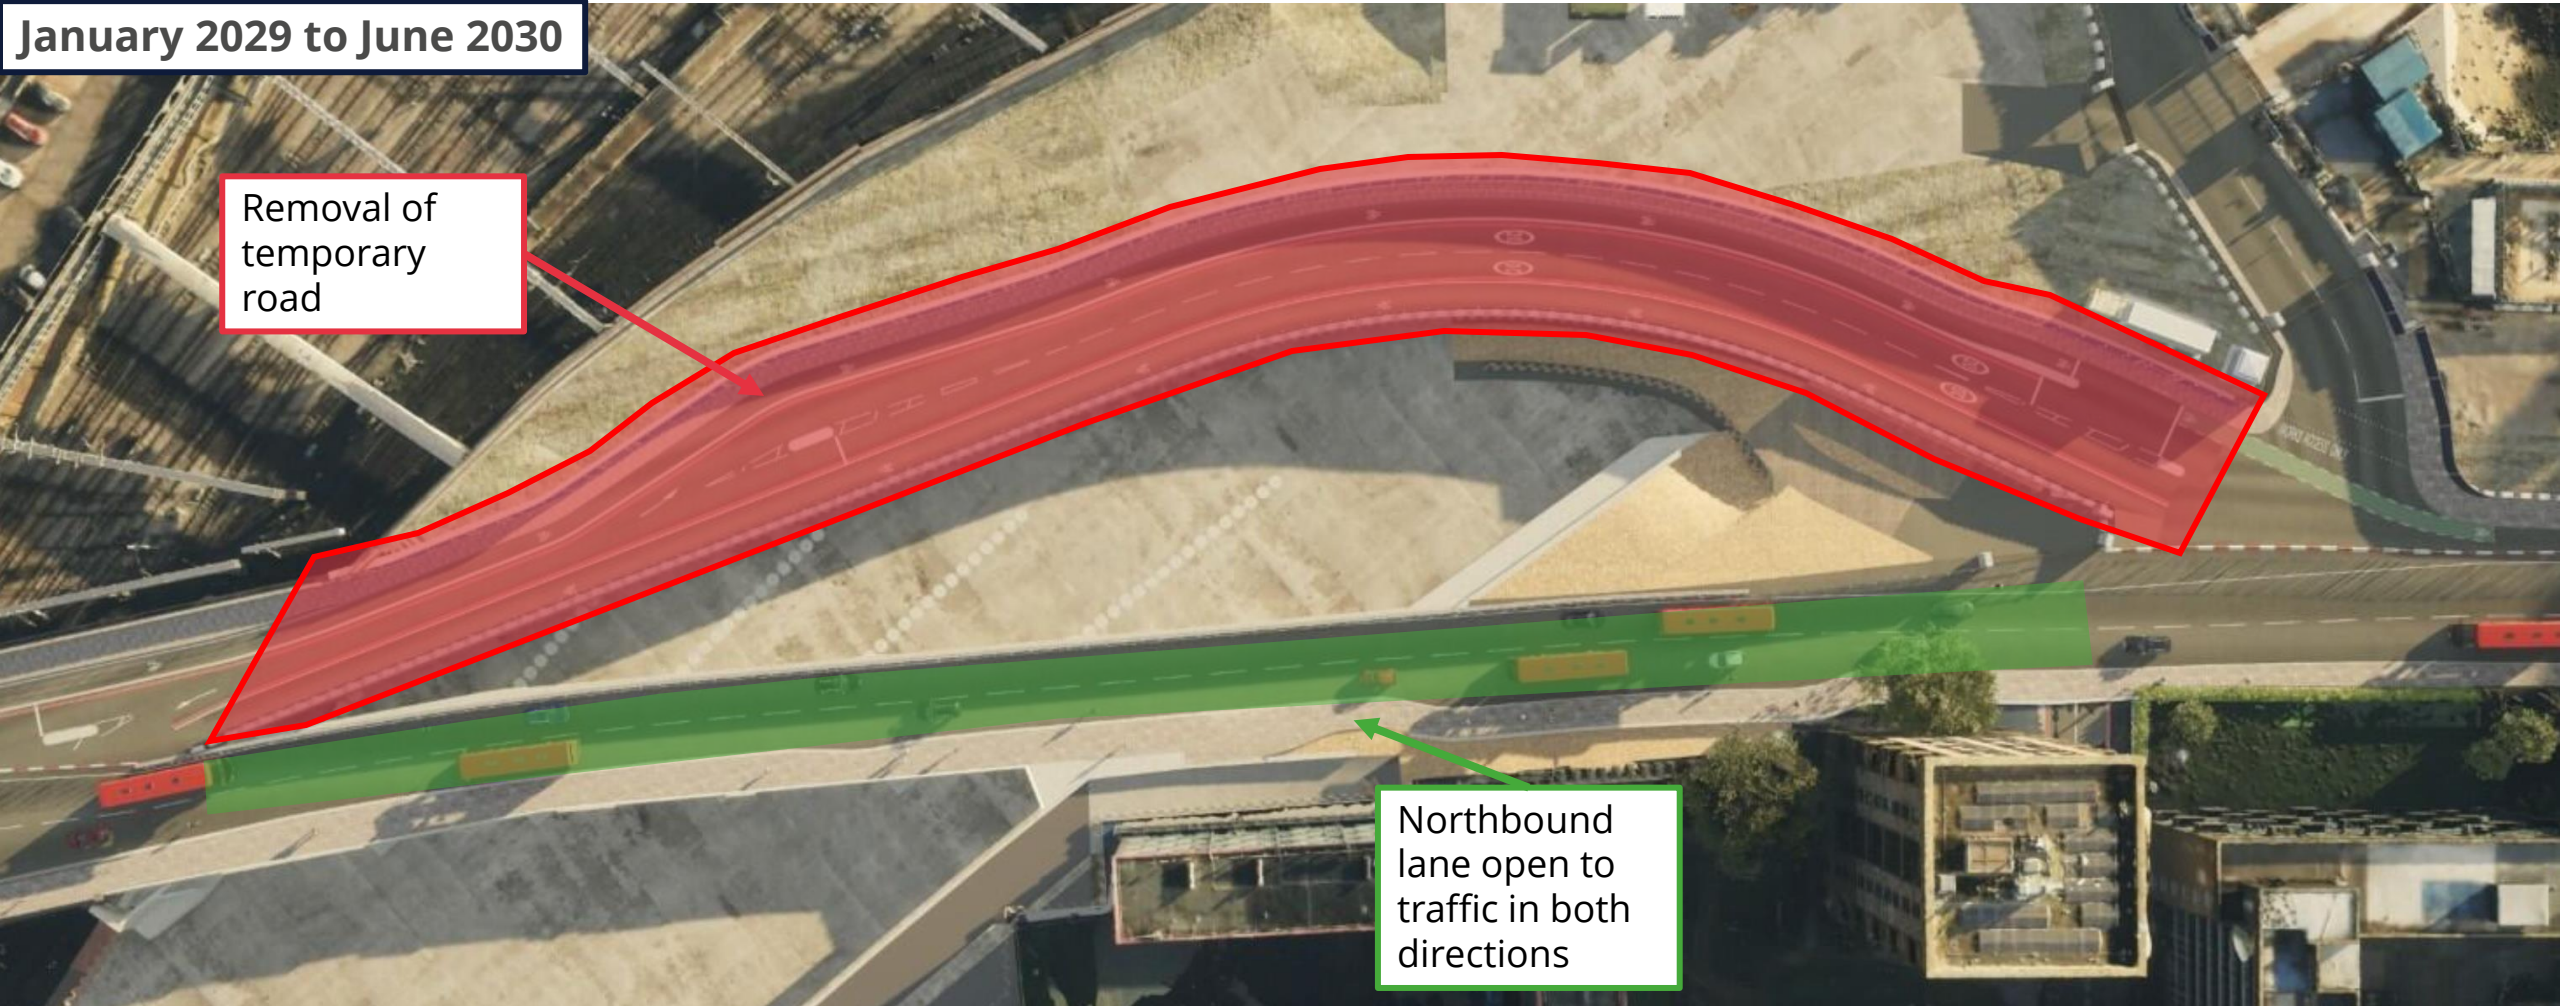

Hampstead Road Bridge – Stage 6 – Southbound Construction

October 2029 to May 2030

Installation of
remaining
northern section
piles


Installation and propping of steel girders for southbound section.

Reinforced concrete works on
bridge deck including

Hampstead Road Bridge – Stage 7 – Casting Stitch

June to July 2030
(4-week closure)

Complete casting stitch
to connect
northbound and
southbound bridge
decks

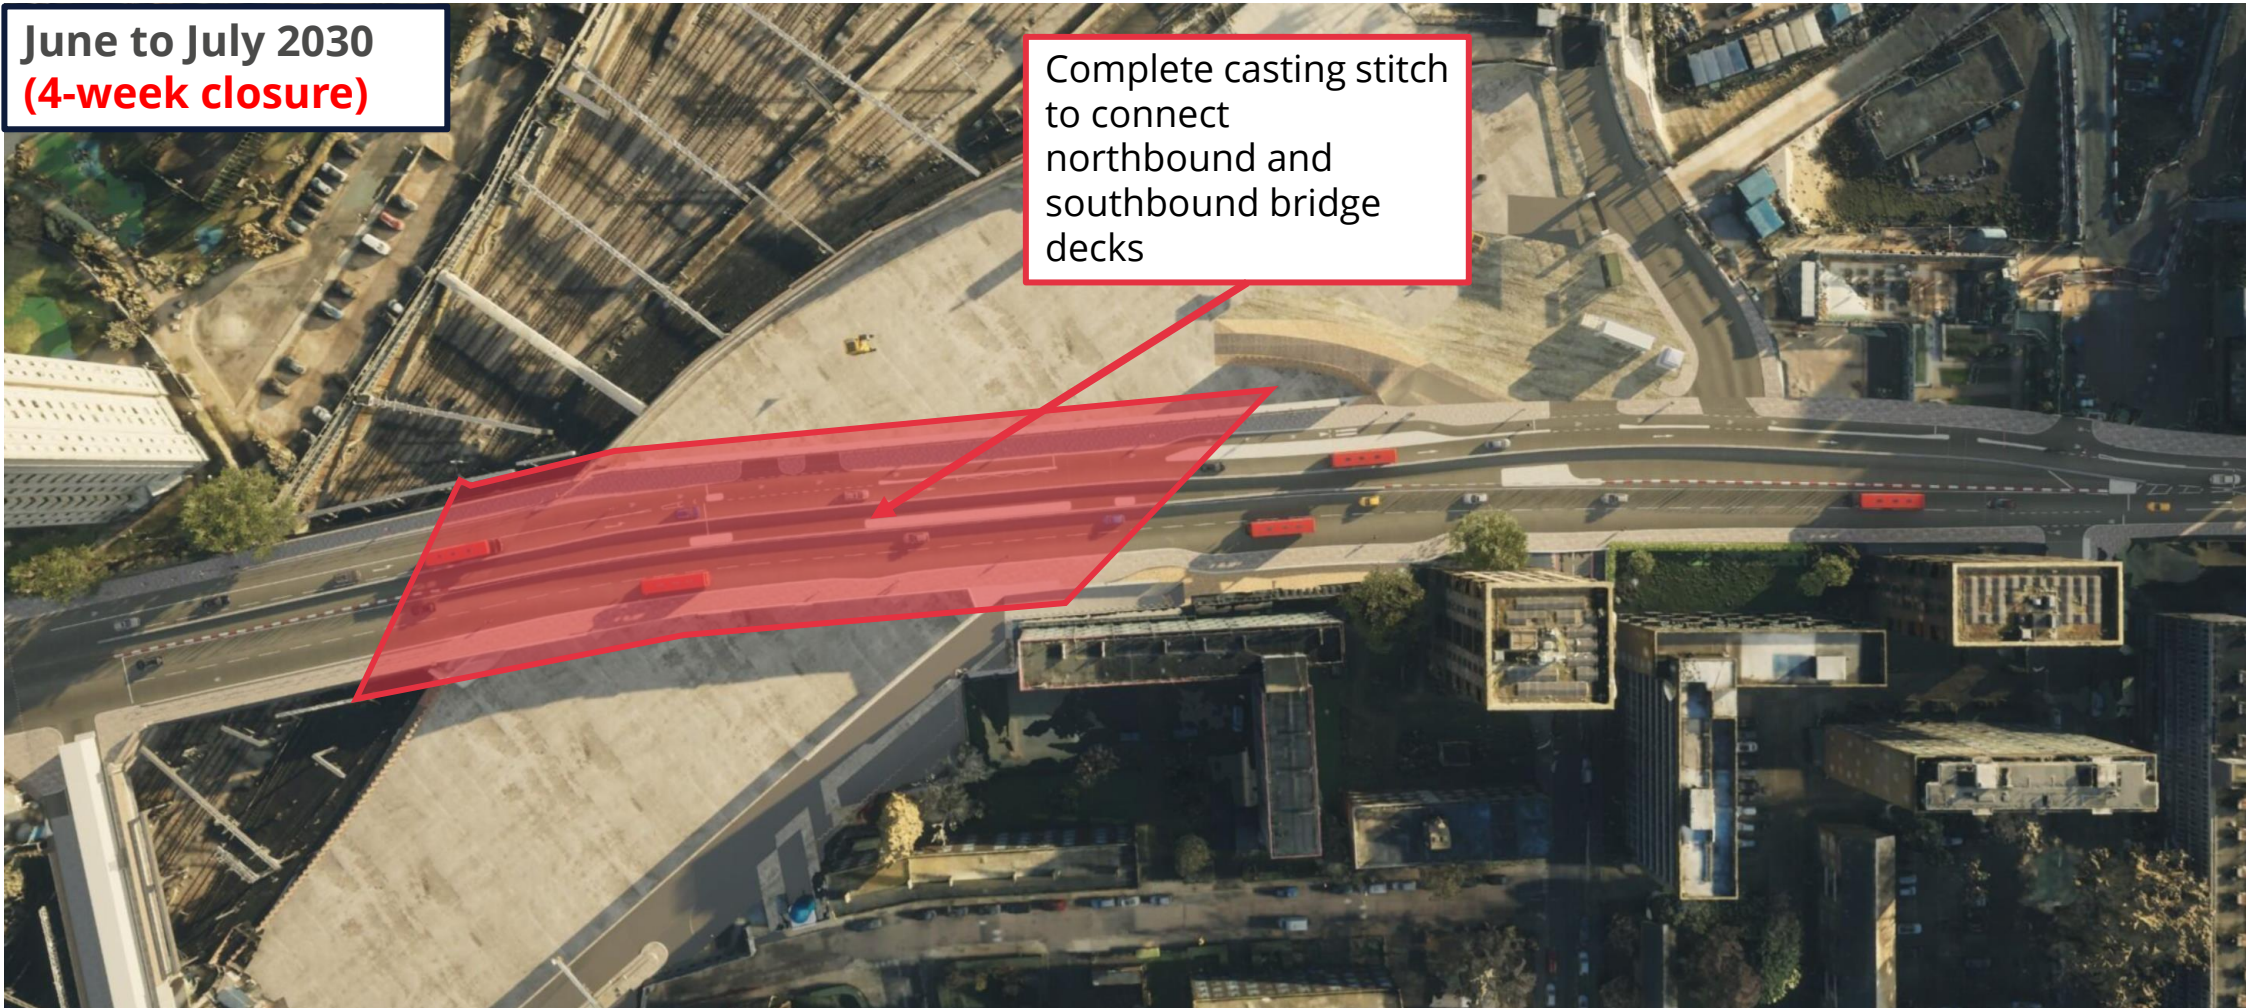

Hampstead Road Bridge – Stage 8a – Base Slab construction

July 2030 to
December 2031



Start excavation to base slab level, which is the level of new railway, and construct reinforced concrete slab

Hampstead Road Bridge – Stage 8b – Finishing Works

June 2030 until
December 2031

Road finishing -
Tarmac, white lining,
and road signs
installed

Removal of traffic
management

Permanent footpath works – waterproofing /
kerbing / drainage / footpath finishing / lighting
columns




Text messaging service

We are launching a new SMS messaging service within the Euston Approaches to share information on our planned works, changes or delays to works, and extended working hours. We will also continue to engage with residents using our regular notices and information on the HS2 website. Each text message will contain a short summary of the key information and a link to the full update on the HS2 website.

Should you wish to receive our SMS updates please complete a short online form [here](#) by providing your name, contact number and street name. You will be able to unsubscribe at any time by following the link provided in each SMS.

Alternatively, you can sign up by scanning the QR code

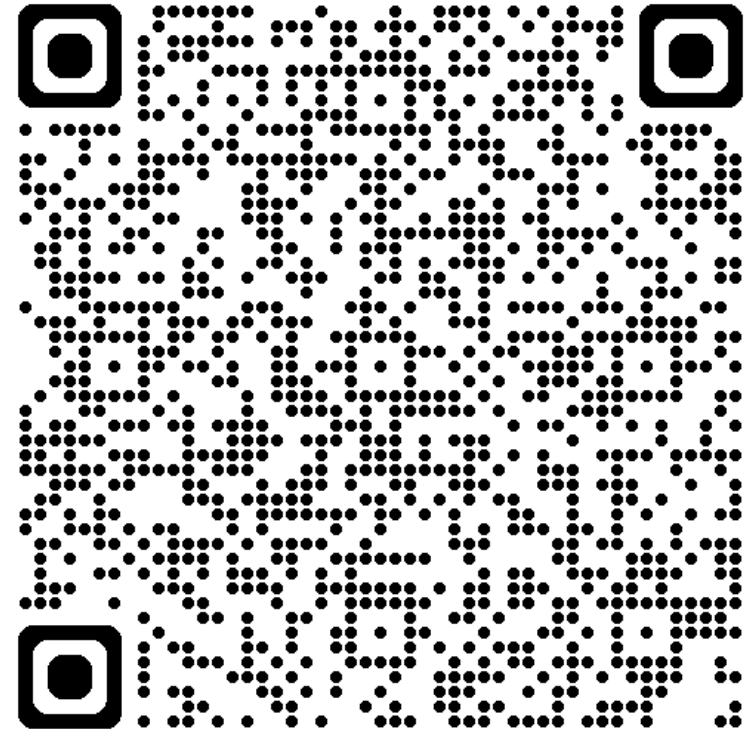

Thank you

